



**THE STATE OF NEW HAMPSHIRE  
DEPARTMENT OF TRANSPORTATION**



*Blank*  
103

**CHRISTOPHER D. CLEMENT, SR.  
COMMISSIONER**

**JEFF BRILLHART, P.E.  
ASSISTANT COMMISSIONER**

Bureau of Construction  
April 9, 2013

Her Excellency, Governor Margaret Wood Hassan  
and the Honorable Council  
State House  
Concord, New Hampshire 03301

**REQUESTED ACTION**

1. Authorize the Department of Transportation to enter into a contract with E.D. Swett, Inc. (Vendor 154176) of Concord, NH on the basis of a low bid of \$4,339,354.90 for replacing two "red list" bridges: the Middle Road (NH Route 33) bridge over the US Route 1 bypass and the Islington Street bridge over the US Route 1 bypass in Portsmouth, from the date of Governor and Council approval through September 18, 2015 unless extended by the Department in accordance with the Standard Specifications. 100% Federal Funds.

Funding is available as follows: FY 2013  
04-96-96-963515-3054  
Consolidated Federal Aid  
400-500870 Highway Contract Payments \$4,339,354.90

2. Further authorize that a contingency in the amount of \$216,967.75 be approved for payment of latent conditions, which may appear during the construction of the project. The contingency requested is 5% of the contract amount.

Funding is available as follows: FY 2013  
04-96-96-963515-3054  
Consolidated Federal Aid  
400-500870 Highway Contract Payments \$216,967.75

**EXPLANATION**

The intent of this project is to replace the Middle Road (NH 33) Bridge over US 1 Bypass and the Islington Street Bridge over US 1 Bypass. This project is the second of four projects that will remove or replace the existing "red list" bridges over the US 1 Bypass in Portsmouth. The existing bridges were constructed around 1940 and are in need of replacement. The project will include 550' of roadway approach work on Middle Road and includes full pavement reconstruction, sidewalk, guardrail and drainage work. The project will also include 750' of roadway approach work on Islington Street that will include full pavement reconstruction, sidewalk, guardrail and drainage work. Work on US 1 Bypass will include pavement rehabilitation, guardrail work, drainage work and construction of a concrete median barrier.

Page 2


The contingency amount is proposed to be 5% of the contract amount. Utility relocations and environmental concerns related to storm water management will increase the risk of overruns.

The Contractor has been prequalified by this Department. The Contract has been approved by the Attorney General as to form and execution, and the Department has certified that the necessary funds are available. Copies of the fully executed contract are on file at the Secretary of State's Office and the Department of Administrative Service's Office, and subsequent to Governor and Council approval will be on file at the Department of Transportation.

This project funding is 80% federal funds with 20% state match. Turnpike toll credit is being utilized for match requirements, effectively using 100% federal funds.

A copy of the Tabulation of Bids received for this project is attached along with the Contract Supplemental Sheet and a map indicating the location of the project.

Sincerely,

Handwritten signature of Christopher D. Clement, Sr. in black ink.

Christopher D. Clement, Sr.  
Commissioner

CDC/md

Department Estimate: \$5,106,663.50  
Contract Amount: \$4,339,354.90  
Under Estimate: \$ 767,308.60

Attachments

March 5, 2013

## SUPPLEMENTAL PROJECT INFORMATION SHEET

**DESCRIPTION:** This project will replace two “Red List” bridges: the Middle Road (NH Route 33) Bridge over the US Route 1 Bypass; and the Islington Street Bridge over the US Route 1 Bypass. The project begins approximately 4,800 feet south of the Portsmouth Traffic Circle and continues north approximately 2,300 feet. The work on the US Route 1 Bypass consists of pavement rehabilitation, guardrail work, drainage work, and the construction of single slope median barrier adjacent to the new bridge piers.

The approach work on Middle Road begins approximately 100 feet west of the intersection with Sheffield Road and continues east approximately 550 feet. The improvements consist of full pavement reconstruction, sidewalk, guardrail, and drainage work.

The approach work on Islington Street begins at the intersection with Barberry Lane and continues east approximately 750 feet. The improvements also consist of full pavement reconstruction, sidewalk, guardrail and drainage work.

**FEDERAL FUNDING:** The Construction funding is from the State’s Ten Year Transportation Improvement Plan with 80% federal funding utilizing Turnpike Toll credits as the State’s 20% match.


**CONTINGENCY:** The contingency amount is proposed to be approximately 5% of the contract amount. Utility relocations and environmental concerns related to storm water management will increase the risk of overruns.

**PROJECT INITIATED:** State Ten-Year Transportation Improvement Program


**PROJECT EXPLANATION:** This project is the second of four projects that will remove or replace the existing “red list” bridges over the US Route 1 Bypass in Portsmouth. The existing bridges were constructed around 1940 and are in need of replacement.

**TRAFFIC IMPLICATION:** During construction, the posted speed limit will be reduced to 35 mph along the US Route 1 Bypass. Two travel lanes (NB and SB) will be maintained on the US Route 1 Bypass whenever possible. Temporary lane or shoulder closures will be permitted during off-peak hours for work operations along the US Route 1 Bypass, Monday through Thursday, with the approval of the Engineer. Temporary shoulder widening will be constructed on the US Route 1 Bypass to facilitate traffic control during the bridge construction. Traffic shall be shut down on the US Route 1 Bypass during the removal of the existing structural steel; erection of the new structural steel; and for any authorized, unprotected work over the travel lanes. Traffic shutdowns will be permitted between the hours of 10:00 PM to 5:00 AM and shall not exceed 15 minutes, with only two 15-minute shutdowns allowed per hour. The Middle Road and Islington Street bridges will be closed during construction. Only one of the bridges can be closed at a time. Detour signage will be provided to direct motorists to alternate routes during the bridge closures. The project also includes alterations to signal timings along the detour routes to facilitate traffic management during the bridge closures.

**FINAL COMPLETION DATE:** Friday, September 18, 2015

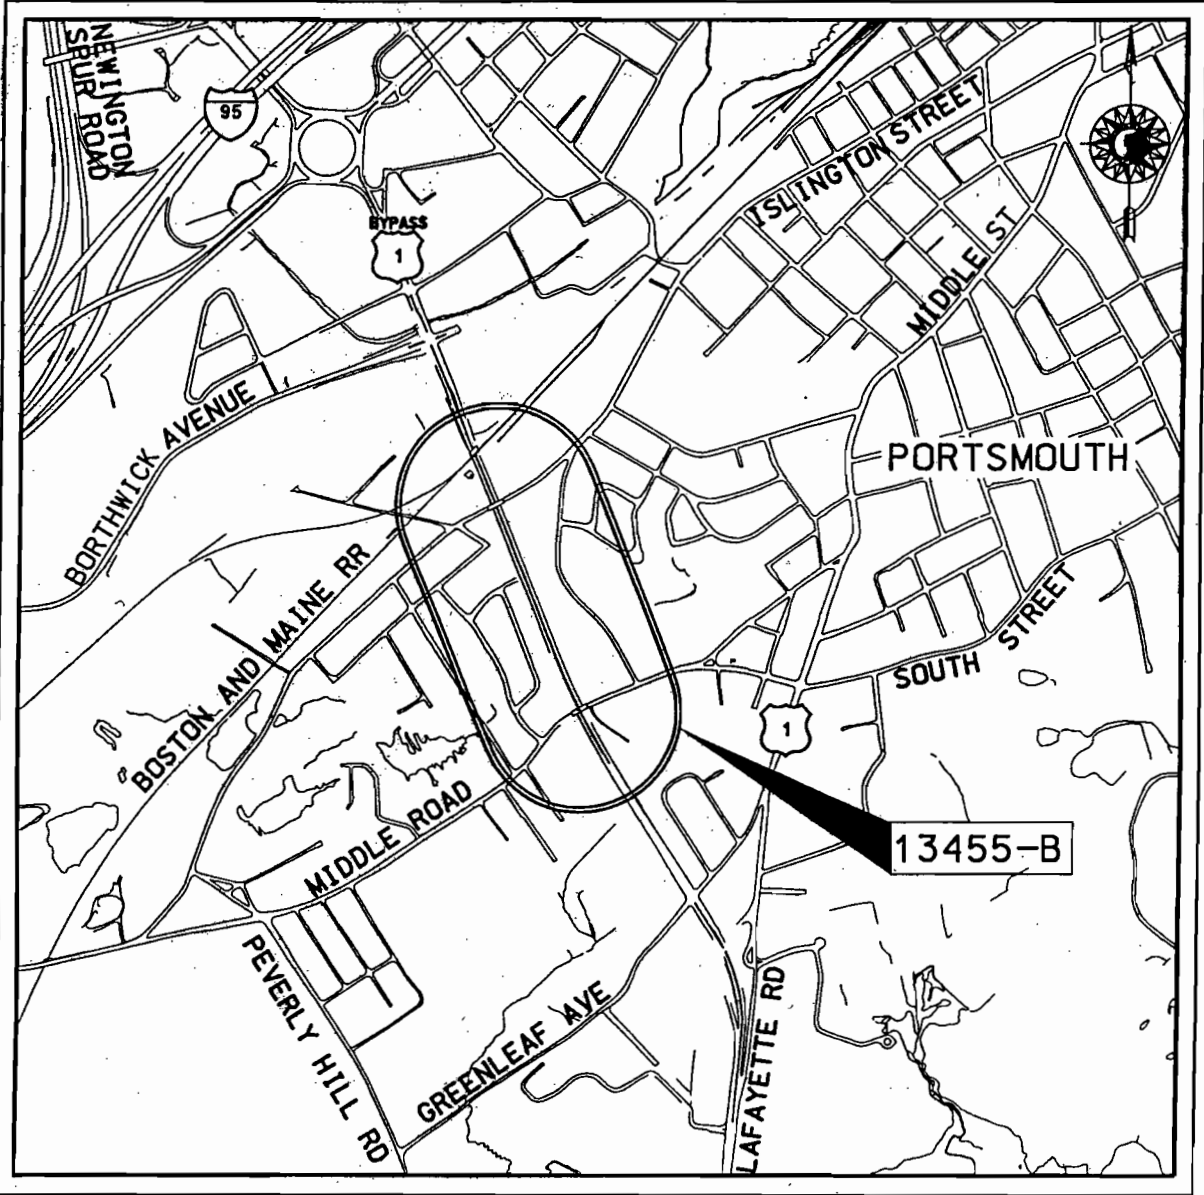

LOCATION MAP



GRAPHIC SCALE

PROJECT: PORTSMOUTH  
X-A000(995), 13455B

COUNTIES AND CODES: ROCKINGHAM 015

DATE BIDS OPEN: APRIL 4, 2013

SCOPE OF WORK: BRIDGE REPLACEMENT

LOCATION: MIDDLE ROAD BRIDGE OVER US ROUTE 1 BYPASS  
AND THE ISLINGTON STREET BRIDGE OVER THE  
US ROUTE 1 BYPASS

COMPLETION DATE: SEPTEMBER 18, 2015

- A E.D. SWETT, INC.  
8 INDUSTRIAL PARK DR., CONCORD, NH 03301 \$ 4,339,354.90
- B SEVERINO TRUCKING CO., INC.  
512 RAYMOND RD., CANDIA, NH 03034 \$ 4,855,612.34
- C WYMAN AND SIMPSON, INC.  
910 MAIN ST., PO BOX 40, RICHMOND, ME 04357 \$ 4,884,222.10
- D R.M. PIPER, INC.  
PO BOX 490, PLYMOUTH, NH 03264 \$ 4,967,719.30
- E MAS BUILDING & BRIDGE, INC.  
18 SHARON AVE., NORFOLK, MA 02056 \$ 4,978,451.55
- F R.S. AUDLEY, INC.  
609 ROUTE 3A, BOW, NH 03304 \$ 5,146,499.80
- G WEAVER BROS. CONST. CO., INC.  
741 ROUTE 3A, BOW, NH 03304 \$ 5,378,259.00
- H CPM CONSTRUCTORS  
PO BOX B, FREEPORT, ME 04032 \$ IRREGULAR

ITEM NO.	DESCRIPTION	UNIT	A			B			C		
			QUANTITY	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL		
201.1	CLEARING AND GRUBBING (F)	A									
201.21	REMOVING SMALL TREES	EA	5.	125.00	625.00	400.00	2,000.00	125.00	625.00		
201.881	INVASIVE SPECIES CONTROL										
201.882	TYPE I	SY	460.	2.00	920.00	1.00	460.00	2.00	920.00		
202.41	INVASIVE SPECIES CONTROL	SY	1,600.	2.00	3,200.00	2.00	3,200.00	2.00	3,200.00		
202.41	REMOVAL OF EXISTING PIPE										
202.5	0-24" DIAMETER	LF	530.	10.00	5,300.00	10.00	5,300.00	10.00	5,300.00		
202.5	REMOVAL OF CATCH BASINS, DROP INLETS, AND MANHOLES										
202.7	REMOVAL OF GUARDRAIL	EA	1.	175.00	175.00	500.00	500.00	175.00	175.00		
203.1	COMMON EXCAVATION	LF	2,900.	1.20	3,480.00	3.00	8,700.00	1.20	3,480.00		
203.2	ROCK EXCAVATION	CY	7,400.	7.50	55,500.00	12.00	88,800.00	8.00	59,200.00		
203.5525	PORTABLE CHANGEBABLE	CY	71.	16.50	1,171.50	65.00	4,615.00	17.00	1,207.00		
203.55261	MESSAGE SIGN PLATFORM INSTALLATION AND REMOVAL OF SWZ - PORTABLE QUEUE TRAILER PLATFORM	U	6.	600.00	3,600.00	1,100.00	6,600.00	600.00	3,600.00		
		U	2.	750.00	1,500.00	750.00	1,500.00	1,500.00	3,000.00		

ITEM NO.	DESCRIPTION	UNIT	QUANTITY	A		B		C	
				UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL
203.55262	INSTALLATION AND REMOVAL OF SWZ - PORTABLE CHANGE MESSAGE SIGN PLATFORM	U	2.	750.00	1,500.00	1,100.00	2,200.00	1,500.00	3,000.00
203.5555	GUARDRAIL 25' EAGRT PLATFORM	U	11.	600.00	6,600.00	1,000.00	11,000.00	600.00	6,600.00
203.6	EMBANKMENT-IN-PLACE (F)	CY	2,799.	3.00	8,397.00	10.00	27,990.00	4.00	11,196.00
206.1	COMMON STRUCTURE EXCAVATION	CY	53.	18.00	954.00	50.00	2,650.00	20.00	1,060.00
206.19	COMMON STRUCTURE EXCAVATION EXPLORATORY	CY	50.	25.00	1,250.00	80.00	4,000.00	25.00	1,250.00
206.2	ROCK STRUCTURE EXCAVATION	CY	135.	16.50	2,227.50	65.00	8,775.00	17.00	2,295.00
209.1	GRANULAR BACKFILL	CY	55.	35.00	1,925.00	35.00	1,925.00	35.00	1,925.00
209.201	GRANULAR BACKFILL (BRIDGE) (F)	CY	463.	35.00	16,205.00	50.00	23,150.00	35.00	16,205.00
209.3	GRANULAR BACKFILL (SAND)	CY	43.	30.00	1,290.00	50.00	2,150.00	30.00	1,290.00
209.4	GRANULAR BACKFILL (GRAV)	CY	228.	35.00	7,980.00	50.00	11,400.00	35.00	7,980.00
211.11	VIBRATION MONITORING SERVICES	HR	200.	115.00	23,000.00	85.00	17,000.00	80.00	16,000.00
214.	FINE GRADING	U	1.	27,000.00	27,000.00	25,000.00	25,000.00	70,000.00	70,000.00
304.1	SAND (F)	CY	631.	21.00	13,251.00	22.00	13,882.00	21.00	13,251.00
304.301	CRUSHED GRAVEL	CY	240.	31.00	7,440.00	35.00	8,400.00	31.00	7,440.00
304.35	CRUSHED GRAVEL FOR DRIVES	CY	130.	33.00	4,290.00	35.00	4,550.00	33.00	4,290.00
304.4	CRUSHED STONE (FINE GRADATION) (F)	CY	1,787.	29.00	51,823.00	30.00	53,610.00	29.00	51,823.00
304.5	CRUSHED STONE (COARSE GRADATION) (F)	CY	630.	29.00	18,270.00	30.00	18,900.00	29.00	18,270.00
403.11	HOT BITUMINOUS PAVEMENT, MACHINE METHOD	TON	2,300.	70.00	161,000.00	70.00	161,000.00	85.00	195,500.00
403.12	HOT BITUMINOUS PAVEMENT, HAND METHOD	TON	380.	105.00	39,900.00	105.00	39,900.00	110.00	41,800.00
403.6	PAVEMENT JOINT ADHESIVE	LF	22,900.	.10	2,290.00	.22	5,038.00	.55	12,595.00
403.911	HOT BITUMINOUS BRIDGE PAVEMENT, 1" BASE COURSE (F)	TON	66.	175.00	11,550.00	175.00	11,550.00	185.00	12,210.00
403.99	TEMPORARY BITUMINOUS PAVEMENT	TON	520.	75.00	39,000.00	75.00	39,000.00	90.00	46,800.00
417.	COLD PLANING BITUMINOUS SURFACES	SY	12,600.	1.50	18,900.00	2.50	31,500.00	4.00	50,400.00
502.101	REMOVAL OF EXISTING BRIDGE STRUCTURE	U	1.	100,000.00	100,000.00	65,000.00	65,000.00	75,000.00	75,000.00
502.102	REMOVAL OF EXISTING BRIDGE STRUCTURE	U	1.	100,000.00	100,000.00	65,000.00	65,000.00	50,000.00	50,000.00
503.301	COFFERDAMS WITH SHEETING LEFT-IN-PLACE	U	1.	50,000.00	50,000.00	40,200.00	40,200.00	75,000.00	75,000.00
503.302	COFFERDAMS WITH SHEETING LEFT-IN-PLACE	U	1.	50,000.00	50,000.00	42,700.00	42,700.00	50,000.00	50,000.00
504.1	COMMON BRIDGE EXCAVATION (F)	CY	1,215.	20.00	24,300.00	20.00	24,300.00	20.00	24,300.00
508.	STRUCTURAL FILL	CY	141.	39.00	5,499.00	40.00	5,640.00	39.00	5,499.00
510.101	PILE DRIVING EQUIPMENT	U	1.	15,000.00	15,000.00	32,400.00	32,400.00	25,000.00	25,000.00

ITEM NO.	DESCRIPTION	UNIT	QUANTITY	A			B			C		
				UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	
510.102	PILE DRIVING EQUIPMENT	U	1.	15,000.00	15,000.00	32,400.00	32,400.00	15,000.00	15,000.00			
510.6101	FURNISHING & DRIVING STEEL BEARING PILES	LB	33,300.	.51	16,983.00	.50	16,650.00	1.00	33,300.00			
510.6102	FURNISHING AND DRIVING STEEL BEARING PILES	LB	37,000.	.51	18,870.00	.50	18,500.00	.95	35,150.00			
510.6502	DRIVING POINTS FOR STEEL BEARING PILES	EA	10.	200.00	2,000.00	100.00	1,000.00	250.00	2,500.00			
510.651	SPECIALIZED DRIVING POINTS FOR STEEL BEARING PILES	EA	10.	400.00	4,000.00	250.00	2,500.00	500.00	5,000.00			
510.9	PILE SPLICES	EA	8.	1.00	8.00	10.00	80.00	10.00	80.00			
520.001	CONCRETE CLASS AAA	CY	14.	725.00	10,150.00	300.00	4,200.00	650.00	9,100.00			
520.02	CONCRETE CLASS AA, ABOVE FOOTINGS (F)	CY	85.	800.00	68,000.00	925.00	78,625.00	900.00	76,500.00			
520.0302	CONCRETE CLASS AA APPROAC SLABS (QC/QA) (F)	CY	148.	400.00	59,200.00	300.00	44,400.00	500.00	74,000.00			
520.1	CONCRETE CLASS A	CY	15.	275.00	4,125.00	350.00	5,250.00	550.00	8,250.00			
520.12	CONCRETE CLASS A, ABOVE FOOTINGS (F)	CY	130.	575.00	74,750.00	600.00	78,000.00	500.00	65,000.00			
520.213	CONCRETE CLASS B, FOOTINGS (ON SOIL) (F)	CY	92.	350.00	32,200.00	230.00	21,160.00	400.00	36,800.00			
520.421	CONCRETE CLASS F, FLOWABLE FILL, EXCAVATABLE	CY	69.	150.00	10,350.00	150.00	10,350.00	100.00	6,900.00			
520.7102	CONCRETE BRIDGE DECK (QC/QA) (F)	CY	181.	750.00	135,750.00	805.00	145,705.00	750.00	135,750.00			
520.7202	CONCRETE BRIDGE DECK (QC/QA) (F)	CY	179.	750.00	134,250.00	805.00	144,095.00	700.00	125,300.00			
528.51	PRESTRESSED CONCRETE DECK PANELS (F)	SF	7,708.	15.00	115,620.00	14.00	107,912.00	15.00	115,620.00			
534.3	WATER REPELLENT (SILANE/ SILOXANE)	GAL	60.	65.00	3,900.00	75.00	4,500.00	66.00	3,960.00			
538.2	BARRIER MEMBRANE, PEEL AN STICK - VERTICAL SURFACE (F)	SY	48.	50.00	2,400.00	50.00	2,400.00	60.00	2,880.00			
538.6	BARRIER MEMBRANE, HEAT WELDED - MACHINE METHOD (F)	SY	1,116.	25.00	27,900.00	19.50	21,762.00	20.00	22,320.00			
541.1	PVC WATERSTOPS, NH TYPE 1 (F)	LF	138.	5.00	690.00	10.00	1,380.00	2.00	276.00			
544.	REINFORCING STEEL (F)	LB	11,064.	1.10	12,170.40	.73	8,076.72	1.10	12,170.40			
544.2	REINFORCING STEEL, EPOXY COATED (F)	LB	175,348.	1.25	219,185.00	1.44	252,501.12	1.00	175,348.00			
544.7	SYNTHETIC FIBER REINFORCEMENT (F)	LB	673.	7.50	5,047.50	7.50	5,047.50	7.50	5,047.50			
547.	SHEAR CONNECTORS (F)	EA	6,440.	5.00	32,200.00	4.20	27,048.00	4.00	25,760.00			
548.21	ELASTOMERIC BEARING ASSEMBLIES (F)	EA	10.	2,000.00	20,000.00	1,075.00	10,750.00	2,000.00	20,000.00			
550.1	STRUCTURAL STEEL (F)	LB	259,220.	1.75	453,635.00	1.80	466,596.00	1.66	430,305.20			
559.412	MODIFIED ELASTOMERIC PLUG TYPE EXPANSION JOINT (20" WIDE) (F)	LF	120.	150.00	18,000.00	148.00	17,760.00	150.00	18,000.00			

ITEM NO.	DESCRIPTION	UNIT	QUANTITY	A			B			C		
				UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL			
562.1	SILICONE JOINT SEALANT (F LF	LF	720.	10.00	7,200.00	7.00	5,040.00	6.00	4,320.00			
563.231	BRIDGE RAIL T3 WITH PROTECTIVE SCREENING	LF	316.	200.00	63,200.00	170.00	53,720.00	170.00	53,720.00			
563.241	BRIDGE RAIL T4 WITH PROTECTIVE SCREENING	LF	316.	230.00	72,680.00	200.00	63,200.00	200.00	63,200.00			
565.232	BRIDGE APPROACH RAIL T3 (STEEL POSTS)	U	4.	5,750.00	23,000.00	4,500.00	18,000.00	4,500.00	18,000.00			
565.242	BRIDGE APPROACH RAIL T4 (STEEL POSTS)	U	4.	6,000.00	24,000.00	5,800.00	23,200.00	6,000.00	24,000.00			
570.4	MORTAR RUBBLE MASONRY (F) CY	CY	4.	500.00	2,000.00	450.00	1,800.00	500.00	2,000.00			
582.1	SLOPE PAVING WITH CONCRETE (F)	SY	686.	55.00	37,730.00	65.00	44,590.00	60.00	41,160.00			
585.3	STONE FILL, CLASS C	CY	40.	30.00	1,200.00	45.00	1,800.00	30.00	1,200.00			
593.421	GEOTEXTILE; PERM CONTROL CL.2, NON-MOVEN	SY	170.	3.00	510.00	2.00	340.00	3.00	510.00			
603.0001	VIDEO INSPECTION	LF	980.	1.00	980.00	1.00	980.00	1.00	980.00			
603.00212	12" R.C. PIPE, 2000D	LF	50.	31.00	1,550.00	42.00	2,100.00	31.00	1,550.00			
603.00215	15" R.C. PIPE, 2000D	LF	220.	42.00	9,240.00	45.00	9,900.00	42.00	9,240.00			
603.00218	18" R.C. PIPE, 2000D	LF	18.	90.00	1,620.00	125.00	2,250.00	90.00	1,620.00			
603.00312	12" R.C. PIPE, 3000D	LF	98.	40.00	3,920.00	42.00	4,116.00	40.00	3,920.00			
603.00315	15" R.C. PIPE, 3000D	LF	480.	43.00	20,640.00	42.00	20,160.00	43.00	20,640.00			
603.00318	18" R.C. PIPE, 3000D	LF	87.	49.00	4,263.00	50.00	4,350.00	49.00	4,263.00			
603.36115	15" ALUMINIZED STEEL END SECTION	EA	1.	200.00	200.00	200.00	200.00	200.00	200.00			
603.36118	18" ALUMINIZED STEEL END SECTION	EA	8.	250.00	2,000.00	225.00	1,800.00	250.00	2,000.00			
603.36124	24" ALUMINIZED STEEL END SECTION	EA	5.	350.00	1,750.00	300.00	1,500.00	350.00	1,750.00			
603.44015	15" CORR. POLYETHYLENE PIPE FOR SLOPE DRAINAGE	LF	45.	40.00	1,800.00	45.00	2,025.00	40.00	1,800.00			
603.99012	12" TEMPORARY DRAIN. PIPE	LF	370.	45.00	16,650.00	40.00	14,800.00	45.00	16,650.00			
603.99015	15" TEMPORARY DRAIN. PIPE	LF	570.	46.00	26,220.00	40.00	22,800.00	46.00	26,220.00			
603.99018	18" TEMPORARY DRAIN PIPE	LF	170.	49.00	8,330.00	50.00	8,500.00	49.00	8,330.00			
604.0007	POLYETHYLENE LINER	EA	13.	130.00	1,690.00	150.00	1,950.00	130.00	1,690.00			
604.12	CATCH BASINS TYPE B TEMPORARY DROP INLETS, TYPE B	U	15.	2,000.00	30,000.00	2,400.00	36,000.00	2,000.00	30,000.00			
604.2429	TEMPORARY DROP INLETS, TYPE B	U	8.	1,700.00	13,600.00	2,000.00	16,000.00	1,700.00	13,600.00			
604.32	DRAINAGE MANHOLES	U	5.	2,000.00	10,000.00	2,100.00	10,500.00	2,000.00	10,000.00			
604.3249	TEMPORARY DRAINAGE MANHOLES	U	3.	2,000.00	6,000.00	2,800.00	8,400.00	2,000.00	6,000.00			
604.4	RECONSTRUCTING/ADJUSTING CATCH BASIN & DROP INLET	LF	2.	300.00	600.00	750.00	1,500.00	300.00	600.00			
606.120	BEAM GUARDRAIL (STANDARD SECTION) (STEEL POST)	LF	1,700.	17.00	28,900.00	16.25	27,625.00	17.00	28,900.00			
606.1255	BEAM GUARDRAIL (TERM. UNIT TYPE EAGRT 25 FT)	U	11.	1,650.00	18,150.00	1,650.00	18,150.00	1,700.00	18,700.00			
606.147	BEAM GUARDRAIL (TERMINAL UNIT TYPE G-2)	U	4.	600.00	2,400.00	500.00	2,000.00	500.00	2,000.00			
606.2120	DOUBLE-FACED BEAM GUARDRAIL (STANDARD SECTION) (STEEL POST)	LF	440.	25.00	11,000.00	24.00	10,560.00	24.00	10,560.00			



ITEM NO.	DESCRIPTION	UNIT	A			B			C		
			QUANTITY	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL		
606.322	DOUBLE FACED TRANSITION RAIL, STEEL POST	U	4.	5,000.00	20,000.00	4,100.00	16,400.00	4,100.00	16,400.00		
606.411	CONCRETE BARRIER, SINGLE-FACED, PRECAST	LF	720.	70.00	50,400.00	80.00	57,600.00	100.00	72,000.00		
606.41231	TRANSITION SINGLE SLOPE CONCRETE BARRIER, PRECAST	U	4.	3,000.00	12,000.00	2,000.00	8,000.00	5,000.00	20,000.00		
606.41232	TRANSITION SINGLE SLOPE CONCRETE BARRIER, TYPE 1 PRECAST	U	4.	7,000.00	28,000.00	6,000.00	24,000.00	10,000.00	40,000.00		
606.417	PORTABLE CONCRETE BARRIER FOR TRAFFIC CONTROL	LF	2,100.	15.00	31,500.00	20.00	42,000.00	20.00	42,000.00		
606.9523	TEMP. IMPACT ATTENUATION DEVICE (NON-REDIRECTIVE)										
608.26	TEST LEVEL 3	U	4.	1,000.00	4,000.00	5,000.00	20,000.00	3,500.00	14,000.00		
608.34	6" CONCRETE SIDEWALK (F)	SY	244.	36.00	8,784.00	45.00	10,980.00	90.00	21,960.00		
608.52	4" REINFORCED CONCRETE SIDEWALK (F)	SY	451.	35.00	15,785.00	42.00	18,942.00	85.00	38,335.00		
609.01	TRUNCATED DOME PAVERS (DETECTABLE WARNING PAVERS)	SY	1.	375.00	375.00	375.00	375.00	550.00	550.00		
609.02	STRAIGHT GRANITE CURB	LF	370.	20.00	7,400.00	17.50	6,475.00	30.00	11,100.00		
609.216	CURVED GRANITE CURB	LF	16.	30.00	480.00	26.00	416.00	40.00	640.00		
609.5	STRAIGHT GRANITE SLOPE CURB 6" HIGH	LF	250.	20.00	5,000.00	16.00	4,000.00	30.00	7,500.00		
609.811	RESET GRANITE CURB BITUMINOUS CURB, TYPE B (4" REVEAL)	LF	1,300.	8.00	10,400.00	10.00	13,000.00	25.00	32,500.00		
609.924	SPECIAL STRAIGHT GRANITE CURB (REVEAL UP TO 24")	LF	250.	5.00	1,250.00	5.00	1,250.00	6.00	1,500.00		
611.05212	12" CEMENT LINED DUCTILE IRON WATER PIPE, CL 52	LF	57.	150.00	8,550.00	55.00	3,135.00	240.00	13,680.00		
611.05216	16" CEMENT LINED DUCTILE IRON WATER PIPE, CL 52	LF	420.	111.00	46,620.00	125.00	52,500.00	111.00	46,620.00		
611.31012	12" GATE VALVE	EA	400.	100.00	40,000.00	150.00	60,000.00	100.00	40,000.00		
611.31016	16" GATE VALVE	EA	2.	2,500.00	5,000.00	2,100.00	4,200.00	2,500.00	5,000.00		
611.35224	24" CASING PIPE WITH 12" DIA CL 52 D.I. M.J. CARRIER PIPE	LF	3.	6,500.00	19,500.00	5,800.00	17,400.00	6,500.00	19,500.00		
611.35230	30" CASING PIPE WITH 16" DIA. RESTRAINED JT CL 52 CARRIER PIPE	LF	80.	370.00	29,600.00	450.00	36,000.00	370.00	29,600.00		
611.42016	20" DUCTILE ADAPTER & 20" X 16" REDUCER	LF	80.	400.00	32,000.00	500.00	40,000.00	400.00	32,000.00		
611.5011	1" COPPER WATER PIPE	EA	1.	6,600.00	6,600.00	2,700.00	2,700.00	6,600.00	6,600.00		
611.5101	1" CORPORATION STOP	LF	260.	33.00	8,580.00	90.00	23,400.00	33.00	8,580.00		
611.5201	1" CURB STOP	EA	5.	570.00	2,850.00	250.00	1,250.00	570.00	2,850.00		
611.70012	12" FITTING	EA	5.	286.00	1,430.00	300.00	1,500.00	286.00	1,430.00		
611.70016	16" FITTING	EA	6.	600.00	3,600.00	850.00	5,100.00	600.00	3,600.00		
611.70020	20" FITTING	EA	6.	1,400.00	8,400.00	1,250.00	7,500.00	1,400.00	8,400.00		
611.743	2" TEMPORARY FLUSHING CONNECTION	EA	1.	2,800.00	2,800.00	1,750.00	1,750.00	2,800.00	2,800.00		
		EA	3.	2,400.00	7,200.00	1,100.00	3,300.00	2,400.00	7,200.00		

ITEM NO.	DESCRIPTION	UNIT	A			B			C		
			QUANTITY	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL		
611.951	WATER MAIN INSULATION	SY	50.	14.00	700.00	10.00	500.00	14.00	700.00		
611.99	4" HPDE TEMPORARY WATER MAIN AND APPURTENANCES	LF	675.	28.00	18,900.00	20.00	13,500.00	28.00	18,900.00		
612.21282	30" DIRECT BURY CASING WITH 16" RESTRAINED JOINT PVC	LF	80.	400.00	32,000.00	500.00	40,000.00	400.00	32,000.00		
612.3104	SEWER MANHOLE, 4 FOOT DIAMETER	VF	60.	470.00	28,200.00	425.00	25,500.00	470.00	28,200.00		
612.3506	6" PVC GRAVITY SEWER SERVICE PIPE	LF	10.	92.00	920.00	125.00	1,250.00	92.00	920.00		
612.3510	10" PVC GRAVITY SEWER PIPE	LF	10.	100.00	1,000.00	150.00	1,500.00	100.00	1,000.00		
612.3515	15" PVC GRAVITY SEWER PIPE	LF	300.	107.00	32,100.00	200.00	60,000.00	107.00	32,100.00		
612.61516	16" PVC GRAVITY SEWER PIPE (RESTRAINED JOINT)	LF	50.	140.00	7,000.00	155.00	7,750.00	140.00	7,000.00		
615.03	TRAFFIC SIGN TYPE C (F)	SF	16.	45.00	720.00	50.00	800.00	33.00	528.00		
615.04	TRAFFIC SIGN TYPE AA (F)	SF	700.	17.00	11,900.00	18.00	12,600.00	19.00	13,300.00		
615.05	TRAFFIC SIGN TYPE BB (F)	SF	12.	75.00	900.00	15.00	180.00	14.00	168.00		
615.30001	BRIDGE MOUNTED TRAFFIC SIGN STRUCTURE	U	1.	8,500.00	8,500.00	7,700.00	7,700.00	16,000.00	16,000.00		
615.30002	BRIDGE MOUNTED TRAFFIC SIGN STRUCTURE	U	1.	8,500.00	8,500.00	7,700.00	7,700.00	15,000.00	15,000.00		
615.30003	BRIDGE MOUNTED TRAFFIC SIGN STRUCTURE	U	1.	8,500.00	8,500.00	7,700.00	7,700.00	15,000.00	15,000.00		
616.191	ALTERATIONS TO TRAFFIC SIGNALS	U	1.	1,200.00	1,200.00	500.00	500.00	1,500.00	1,500.00		
616.192	ALTERATIONS TO TRAFFIC SIGNALS	U	1.	1,200.00	1,200.00	500.00	500.00	1,500.00	1,500.00		
618.61	UNIFORMED OFFICERS WITH VEHICLE	\$	1.	92,000.00	92,000.00	92,000.00	92,000.00	92,000.00	92,000.00		
618.7	FLAGGERS	HR	200.	20.00	4,000.00	30.00	6,000.00	22.00	4,400.00		
619.1	MAINTENANCE OF TRAFFIC PORTABLE CHANGEABLE	U	1.	110,000.00	110,000.00	150,000.00	150,000.00	111,000.00	111,000.00		
619.25	MESSAGE SIGN	U	4.	5,000.00	20,000.00	15,000.00	60,000.00	600.00	2,400.00		
619.253	PORTABLE CHANGEABLE MESSAGE SIGN (UNIT WEEK)	UWK	16.	100.00	1,600.00	300.00	4,800.00	175.00	2,800.00		
619.501	SMART WORK ZONE DEPLOYMENT	U	1.	4,500.00	4,500.00	4,500.00	4,500.00	5,000.00	5,000.00		
619.502	SMART WORK ZONE OPERATIONAL COSTS (WINTER)	MON	8.	250.00	2,000.00	250.00	2,000.00	250.00	2,000.00		
619.503	SMART WORK ZONE OPERATIONAL COSTS (SUMMER)	MON	19.	80.00	1,520.00	80.00	1,520.00	80.00	1,520.00		
619.51	PORTABLE QUEUE TRAILER / SENSOR (POT)	MON	54.	525.00	28,350.00	525.00	28,350.00	525.00	28,350.00		
619.52	PORTABLE CHANGEABLE MESSAGE SIGNS (PCMS)	MON	54.	695.00	37,530.00	695.00	37,530.00	695.00	37,530.00		

ITEM NO.	DESCRIPTION	UNIT	QUANTITY	A		B		C	
				UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL
619.91	RELOCATE SMART WORK ZONE	U	4.	245.00	980.00	245.00	980.00	245.00	980.00
621.1	DETECTIVE MEDIUM	EA	16.	5.00	80.00	15.00	240.00	15.00	240.00
621.2	RETROREFLECTIVE BEAM	EA	58.	5.00	290.00	4.00	232.00	4.00	232.00
622.1	STEEL WITNESS MARKERS	EA	18.	30.00	540.00	25.00	450.00	25.00	450.00
622.2	CONCRETE BOUNDS	EA	15.	300.00	4,500.00	325.00	4,875.00	325.00	4,875.00
628.1	SAWED CONCRETE PAVEMENT	LF	390.	2.70	1,053.00	4.00	1,560.00	3.00	1,170.00
628.2	SAWED BITUMINOUS PAVEMENT	LF	4,000.	1.10	4,400.00	2.00	8,000.00	1.25	5,000.00
632.0104	RETROREFLECTIVE PAINT	LF	52,400.	.12	6,288.00	.12	6,288.00	.12	6,288.00
632.911	OBLITERATE PAVE. MARKING	LF	4,800.	.40	1,920.00	.40	1,920.00	.40	1,920.00
641.	LOAM	CY	460.	19.00	8,740.00	50.00	23,000.00	20.00	9,200.00
643.22	FERTILIZER FOR	TON	1.	750.00	750.00	750.00	750.00	750.00	750.00
645.2535	REFERTILIZATION	TON	1.	750.00	750.00	750.00	750.00	750.00	750.00
645.3	COIR FIBER MATTING FOR	SY	1,400.	6.00	8,400.00	3.25	4,550.00	5.95	8,330.00
645.44	EROSION CONTROL	TON	1,200.	21.00	25,200.00	20.00	24,000.00	21.00	25,200.00
645.45	TEMPORARY SLOPE	SY	13,700.	1.85	25,345.00	1.75	23,975.00	1.85	25,345.00
645.531	STABILIZATION TYPE D (WILDLIFE FRIENDLY)	SY	1,900.	3.25	6,175.00	3.25	6,175.00	3.25	6,175.00
645.7	PERMANENT CHANNEL	LF	3,200.	3.00	9,600.00	3.00	9,600.00	3.00	9,600.00
645.71	STABILIZATION TYPE A	U	1.	5,000.00	5,000.00	15,000.00	15,000.00	5,000.00	5,000.00
645.81	STORM WATER POLLUTION PREVENTION PLAN	HR	510.	40.00	20,400.00	52.50	26,775.00	55.00	28,050.00
646.3	EROSION AND SEDIMENT CONTROLS	HR	80.	100.00	8,000.00	90.00	7,200.00	125.00	10,000.00
647.1	STORMWATER REMOVAL - TRUCKING	A	3.	1,800.00	5,400.00	1,800.00	5,400.00	1,800.00	5,400.00
648.	MULCH AND TACKIFIERS	CY	420.	14.00	5,880.00	40.00	16,800.00	14.00	5,880.00
670.104	SOD	SY	1,900.	4.50	8,550.00	4.50	8,550.00	4.50	8,550.00
692.	TEMPORARY PORTABLE LIGHTING	U	4.	5,000.00	20,000.00	20,000.00	80,000.00	25,000.00	100,000.00
693.	MOBILIZATION	U	1.	211,400.00	211,400.00	410,000.00	410,000.00	480,000.00	480,000.00
697.11	ON-THE-JOB TRAINING OF UNSKILLED WORKERS	\$	1.	600.00	600.00	600.00	600.00	600.00	600.00
697.41	INVASIVE SPECIES CONTROL AND MANAGEMENT PLAN	U	1.	1,500.00	1,500.00	1,750.00	1,750.00	1,000.00	1,000.00
698.12	CRITICAL PATH METHOD (CPM) ELECTRONIC SCHEDULE	U	1.	500.00	500.00	15,000.00	15,000.00	4,500.00	4,500.00
698.2	FIELD OFFICE TYPE B PHYSICAL TESTING	MON	29.	1,500.00	43,500.00	550.00	15,950.00	1,600.00	46,400.00
	LABORATORY	MON	27.	400.00	10,800.00	350.00	9,450.00	800.00	21,600.00

ITEM NO.	DESCRIPTION	UNIT	QUANTITY	A		B		C	
				UNIT PRICE	TOTAL	UNIT PRICE	TOTAL	UNIT PRICE	TOTAL
699.	MISCELLANEOUS TEMPORARY EROSION AND SEDIMENT CONTROL	\$	1.	80,000.00	80,000.00	80,000.00	80,000.00	80,000.00	80,000.00
1010.15	FUEL ADJUSTMENT	\$	1.	70,000.00	70,000.00	70,000.00	70,000.00	70,000.00	70,000.00
1010.2	ASPHALT CEMENT ADJUSTMENT	\$	1.	10,000.00	10,000.00	10,000.00	10,000.00	10,000.00	10,000.00
1010.41	QUALITY CONTROL QUALITY ASSURANCE (QC/QA FOR CONCRETE	\$	1.	10,000.00	10,000.00	10,000.00	10,000.00	10,000.00	10,000.00
					\$4,339,354.90		\$4,855,612.34		\$4,884,222.10

ACORD™

## CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)

04/05/2013

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

**IMPORTANT:** If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER USI Insurance Svcs of NE, Inc. PO Box 6360 Manchester, NH 03108-6360 603 625-1100	CONTACT NAME:		
	PHONE (A/C, No, Ext):	603 625-1100	FAX (A/C, No):
INSURED E D Swett, Inc. 8 Industrial Park Drive Concord, NH 03301	E-MAIL ADDRESS:		
	INSURER(S) AFFORDING COVERAGE		NAIC #
	INSURER A:	Travelers Indemnity Company	25658
	INSURER B:	Travelers Indemnity Company of	25682
	INSURER C:		
	INSURER D:		
	INSURER E:		
	INSURER F:		

COVERAGES CERTIFICATE NUMBER: REVISION NUMBER: 1

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL SUBR INSR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	GENERAL LIABILITY <input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR  GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC		DTCO6C102548IND13	01/01/2013	01/01/2014	EACH OCCURRENCE \$2,000,000 DAMAGE TO RENTED PREMISES (Ea occurrence) \$300,000 MED EXP (Any one person) \$5,000 PERSONAL & ADV INJURY \$1,000,000 GENERAL AGGREGATE \$2,000,000 PRODUCTS - COMP/OP AGG \$2,000,000 \$
A	AUTOMOBILE LIABILITY <input checked="" type="checkbox"/> ANY AUTO ALL OWNED AUTOS <input checked="" type="checkbox"/> HIRED AUTOS <input type="checkbox"/> SCHEDULED AUTOS <input checked="" type="checkbox"/> NON-OWNED AUTOS		DT8107C282320COF13	01/01/2013	01/01/2014	COMBINED SINGLE LIMIT (Ea accident) \$1,000,000 BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$ \$
A	<input checked="" type="checkbox"/> UMBRELLA LIAB' <input type="checkbox"/> EXCESS LIAB' <input type="checkbox"/> OCCUR <input type="checkbox"/> CLAIMS-MADE DED <input checked="" type="checkbox"/> RETENTION \$10000		DTSMCUP7C282332TIL	01/01/2013	01/01/2014	EACH OCCURRENCE \$5,000,000 AGGREGATE \$5,000,000 \$
B	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? <input type="checkbox"/> Y <input checked="" type="checkbox"/> N (Mandatory in NH) If yes, describe under DESCRIPTION OF OPERATIONS below	N/A	DTKUB5389B08813	01/01/2013	01/01/2014	<input checked="" type="checkbox"/> WC STATUTORY LIMITS <input type="checkbox"/> OTH-ER E.L. EACH ACCIDENT \$1,000,000 E.L. DISEASE - EA EMPLOYEE \$1,000,000 E.L. DISEASE - POLICY LIMIT \$1,000,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (Attach ACORD 101, Additional Remarks Schedule, if more space is required)

**\*\*Workers Compensation\*\* NH**

RE: Project: Portsmouth, 13455B X-A000(995). The General Liability policy includes a blanket automatic Additional Insured endorsement that provides Additional Insured status to the Certificate Holder only when there is a written contract that requires such status, and only with regard to work performed on behalf of the named insured.

## CERTIFICATE HOLDER

## CANCELLATION

New Hampshire Department of  
Transportation  
7 Hazen Drive  
PO Box 483  
Concord, NH 03302-0483

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.

AUTHORIZED REPRESENTATIVE

*E. David Jones*

© 1988-2010 ACORD CORPORATION. All rights reserved.

ACORD™

## CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)  
04/10/2013

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER <b>USI Insurance Services LLC</b> PO Box 6360 Manchester, NH 03108-6360 603 625-1100	CONTACT NAME:		
	PHONE (A/C, No, Ext):	603 625-1100	FAX (A/C, No):
	E-MAIL ADDRESS:		
	INSURER(S) AFFORDING COVERAGE		NAIC #
	INSURER A:	Travelers Indemnity Company	25658
INSURED <b>NH Department of Transportation</b> C/O E D Swett, Inc. 8 Industrial Park Drive Concord, NH 03301	INSURER B:		
	INSURER C:		
	INSURER D:		
	INSURER E:		
	INSURER F:		

## COVERAGES

## CERTIFICATE NUMBER:

## REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.


INSR LTR	TYPE OF INSURANCE	ADDL INSR	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS	
A	GENERAL LIABILITY <input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR <input checked="" type="checkbox"/> OCP GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PROJECT <input type="checkbox"/> LOC	X		PRS3C486429IND	04/08/2013	09/18/2015	EACH OCCURRENCE	\$2,000,000
							DAMAGE TO RENTED PREMISES (Ea occurrence)	\$
							MED EXP (Any one person)	\$
							PERSONAL & ADV INJURY	\$
							GENERAL AGGREGATE	\$3,000,000
							PRODUCTS - COMP/OP AGG	\$
								\$
	AUTOMOBILE LIABILITY <input type="checkbox"/> ANY AUTO <input type="checkbox"/> ALL OWNED AUTOS <input type="checkbox"/> HIRED AUTOS <input type="checkbox"/> SCHEDULED AUTOS <input type="checkbox"/> NON-OWNED AUTOS						COMBINED SINGLE LIMIT (Ea accident)	\$
							BODILY INJURY (Per person)	\$
							BODILY INJURY (Per accident)	\$
							PROPERTY DAMAGE (Per accident)	\$
								\$
	UMBRELLA LIAB <input type="checkbox"/> EXCESS LIAB DED RETENTION \$						EACH OCCURRENCE	\$
							AGGREGATE	\$
								\$
	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) If yes, describe under DESCRIPTION OF OPERATIONS below						WC STATUTORY LIMITS	OTHER
							E.L. EACH ACCIDENT	\$
							E.L. DISEASE - EA EMPLOYEE	\$
							E.L. DISEASE - POLICY LIMIT	\$

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (Attach ACORD 101, Additional Remarks Schedule, if more space is required)

RE: Middle Road & Islington Street, bridge replacements over U.S. Route 1 By-Pass. Project No. 13455B  
RE: Project: Portsmouth, 13455B X-A000(995). The General Liability policy includes a blanket automatic Additional Insured endorsement that provides Additional Insured status to the Certificate Holder only when there is a written contract that requires such status, and only with regard to work performed on behalf of the named insured.

## CERTIFICATE HOLDER

## CANCELLATION

<b>New Hampshire Department of Transportation</b> 7 Hazen Drive PO Box 483 Concord, NH 03302-0483	SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.
	AUTHORIZED REPRESENTATIVE  

© 1988-2010 ACORD CORPORATION. All rights reserved.
