



**THE STATE OF NEW HAMPSHIRE**  
**DEPARTMENT OF TRANSPORTATION**



*Beaulac*  
*30*

**JEFF BRILLHART, P.E.**  
**ACTING COMMISSIONER**

Bureau of Construction  
 December 12, 2014

Her Excellency, Governor Margaret Wood Hassan  
 and the Honorable Council  
 State House  
 Concord, New Hampshire 03301

**REQUESTED ACTION**

1. Authorize the Department of Transportation to enter into a contract with Beck & Bellucci, Inc. (Vendor 160421) of Franklin, NH on the basis of a low bid of \$1,572,551.00 for the rapid bridge deck replacement of the US Route 3/NH 11 bypass over NH Route 11A in Gilford, from the date of Governor and Council approval through August 5, 2016 unless extended by the Department in accordance with the Standard Specifications. 100% Federal Funds.

Funding is available as follows for FY 2015 and is contingent upon the availability and continued appropriation of FY 2016 funds.

Funding is available as follows:	<u>FY 2015</u>	<u>FY 2016</u>
04-96-96-963515-3054		
Consolidated Federal Aid		
400-500870 Highway Contract Payments	\$800,000.00	\$772,551.00

2. Further authorize that a contingency in the amount of \$157,255.10 be approved for payment of latent conditions, which may appear during the construction of the project. The contingency requested is 10% of the contract amount.

Funding is available as follows:	<u>FY 2015</u>
04-96-96-963515-3054	
Consolidated Federal Aid	
400-500870 Highway Contract Payments	\$157,255.10

**EXPLANATION**

This project is part of the annual Bridge Rehabilitation, Preservation Improvement Program (BRPI). The existing bridge was built in 1965 and is currently on the State's red list (#43) due to the "poor" rating of the deck. The work involves replacing the poor condition bridge deck by installing full width, full depth deck panels. The innovative treatment, with transversely pre-tensioning and longitudinal post tensioning, is partially funded by a federal Innovative Bridge Research and Technology Grant. The bridge deck will be placed during a 60 hour closure of the road, with traffic temporarily diverted along the interchange ramps. Minor bridge maintenance work has been done on the bridge including cleaning and painting of steel in 1981 and 1992, and steel sliding plate expansion joint removal in 1997. The proposed bridge deck replacement will extend the life of the structure and remove it from the red list.

The contingency amount is proposed to be 10% of the contract amount. Due to the nature of the bridge work and the inability to see areas of the bridge that will become exposed when the deck is off, (top of abutments and under wing caps) increases the risks of costs overruns. Also spot surveying of elevations revealed that the original plan elevations differ from those in the field and the Contractor may need to make field adjustments to complete the work.

Although the bid costs exceeded the Department's estimate, the low bid is felt to be reasonable for the work involved. This is an innovative bridge deck treatment with some uncertainty from the industry. The project was previously advertised but was not awarded when bids significantly exceeded the estimate. The Department then worked with UNH to pilot test sections of the panels and build confidence in the industry to then readvertise the project using this technology. Readvertising this project would result, in our opinion, in higher prices and prevent the completion of the work in a timely manner. The Department considers it to be in the best interest of the State to accept this bid to accomplish these needed repairs.

The Contractor has been prequalified by this Department. The Contract has been approved by the Attorney General as to form and execution, and the Department has certified that the necessary funds are available and that the bid reasonably conforms to the engineer's estimate in accordance with State procedure. Copies of the fully executed contract are on file at the Secretary of State's Office and the Department of Administrative Service's Office, and subsequent to Governor and Council approval will be on file at the Department of Transportation.

This project funding is 80% federal funds with 20% state match. Turnpike toll credit is being utilized for match requirements, effectively using 100% federal funds.

A copy of the Tabulation of Bids received for this project is attached along with the Contract Supplemental Sheet and a map indicating the location of the project.

Sincerely,



David J. Brillhart, P.E.  
Acting Commissioner

DJB/md

Department Estimate: \$1,528,446.50  
Contract Amount: \$1,572,551.00  
Over Estimate: \$ 44,104.50

Attachments

October 15, 2014

## SUPPLEMENTAL PROJECT INFORMATION SHEET

**DESCRIPTION:** This project consists of the rapid bridge deck replacement of the US Route 3/NH Route 11 Bypass over NH Route 11A. Partial funding for the project is through an Innovative Bridge Research and Deployment grant. This shall include removing and replacing the bridge deck, u-back wing copings, abutment joints, and bridge rail. Full depth, full width deck panels, pre-tensioned transversely and post-tensioned longitudinally, will be used to construct the new deck. The Contractor will have a 60 hour window closure period of US 3/NH 11 Bypass over NH 11A for bridge deck removal and replacement. Roadwork consists of minor pavement approach work and the replacement of bridge approach rail. Drainage structures near the bridge will be raised to accommodate the 2 ½" profile grade change on the bridge.

**FEDERAL FUNDING:** \$283,250 is 100% Federal (Innovative Bridge Research and Development (IBRD)) with the balance being 80% Federal with the State's 20% match being Turnpike Toll Credits


**CONTINGENCY:** The Contingency amount is proposed to be 10%. Due to the nature of the bridge work and the inability to see areas of the bridge that will become exposed when the deck is off (top of abutments and under wing caps) increases the risks of costs overruns. Also spot surveying of elevations revealed that the original plan elevations differ from those in the field and the Contractor may need to make field adjustments to complete the work.

**PROJECT INITIATED:** State's 10-Year Transportation Improvement Program

**PROJECT EXPLANATION:** The existing bridge was built in 1965 and is currently on the State's red list (#43) due to the "poor" rating of the deck. Minor bridge maintenance work has been done on the bridge including cleaning and painting of steel in 1981 and 1992, and steel sliding plate expansion joint removal in 1997. The proposed bridge deck replacement will extend the life of the structure and remove it from the red list.

**TRAFFIC IMPLICATIONS:** During the 60 hour closure, traffic will be diverted around the site utilizing diversion roundabouts near the gores of the on and off ramps. Signing will be used to divert this traffic. Once traffic is back on the bridge, but before the bridge rail is constructed, a minimum of two 12-foot lanes will be maintained on the bypass. During membrane and paving operations, one lane may need to be detoured to the on and off ramps while the other lane stays on half of the bridge to avoid alternating one-way traffic on the bypass.

**COMPLETION DATE:** August 5, 2016

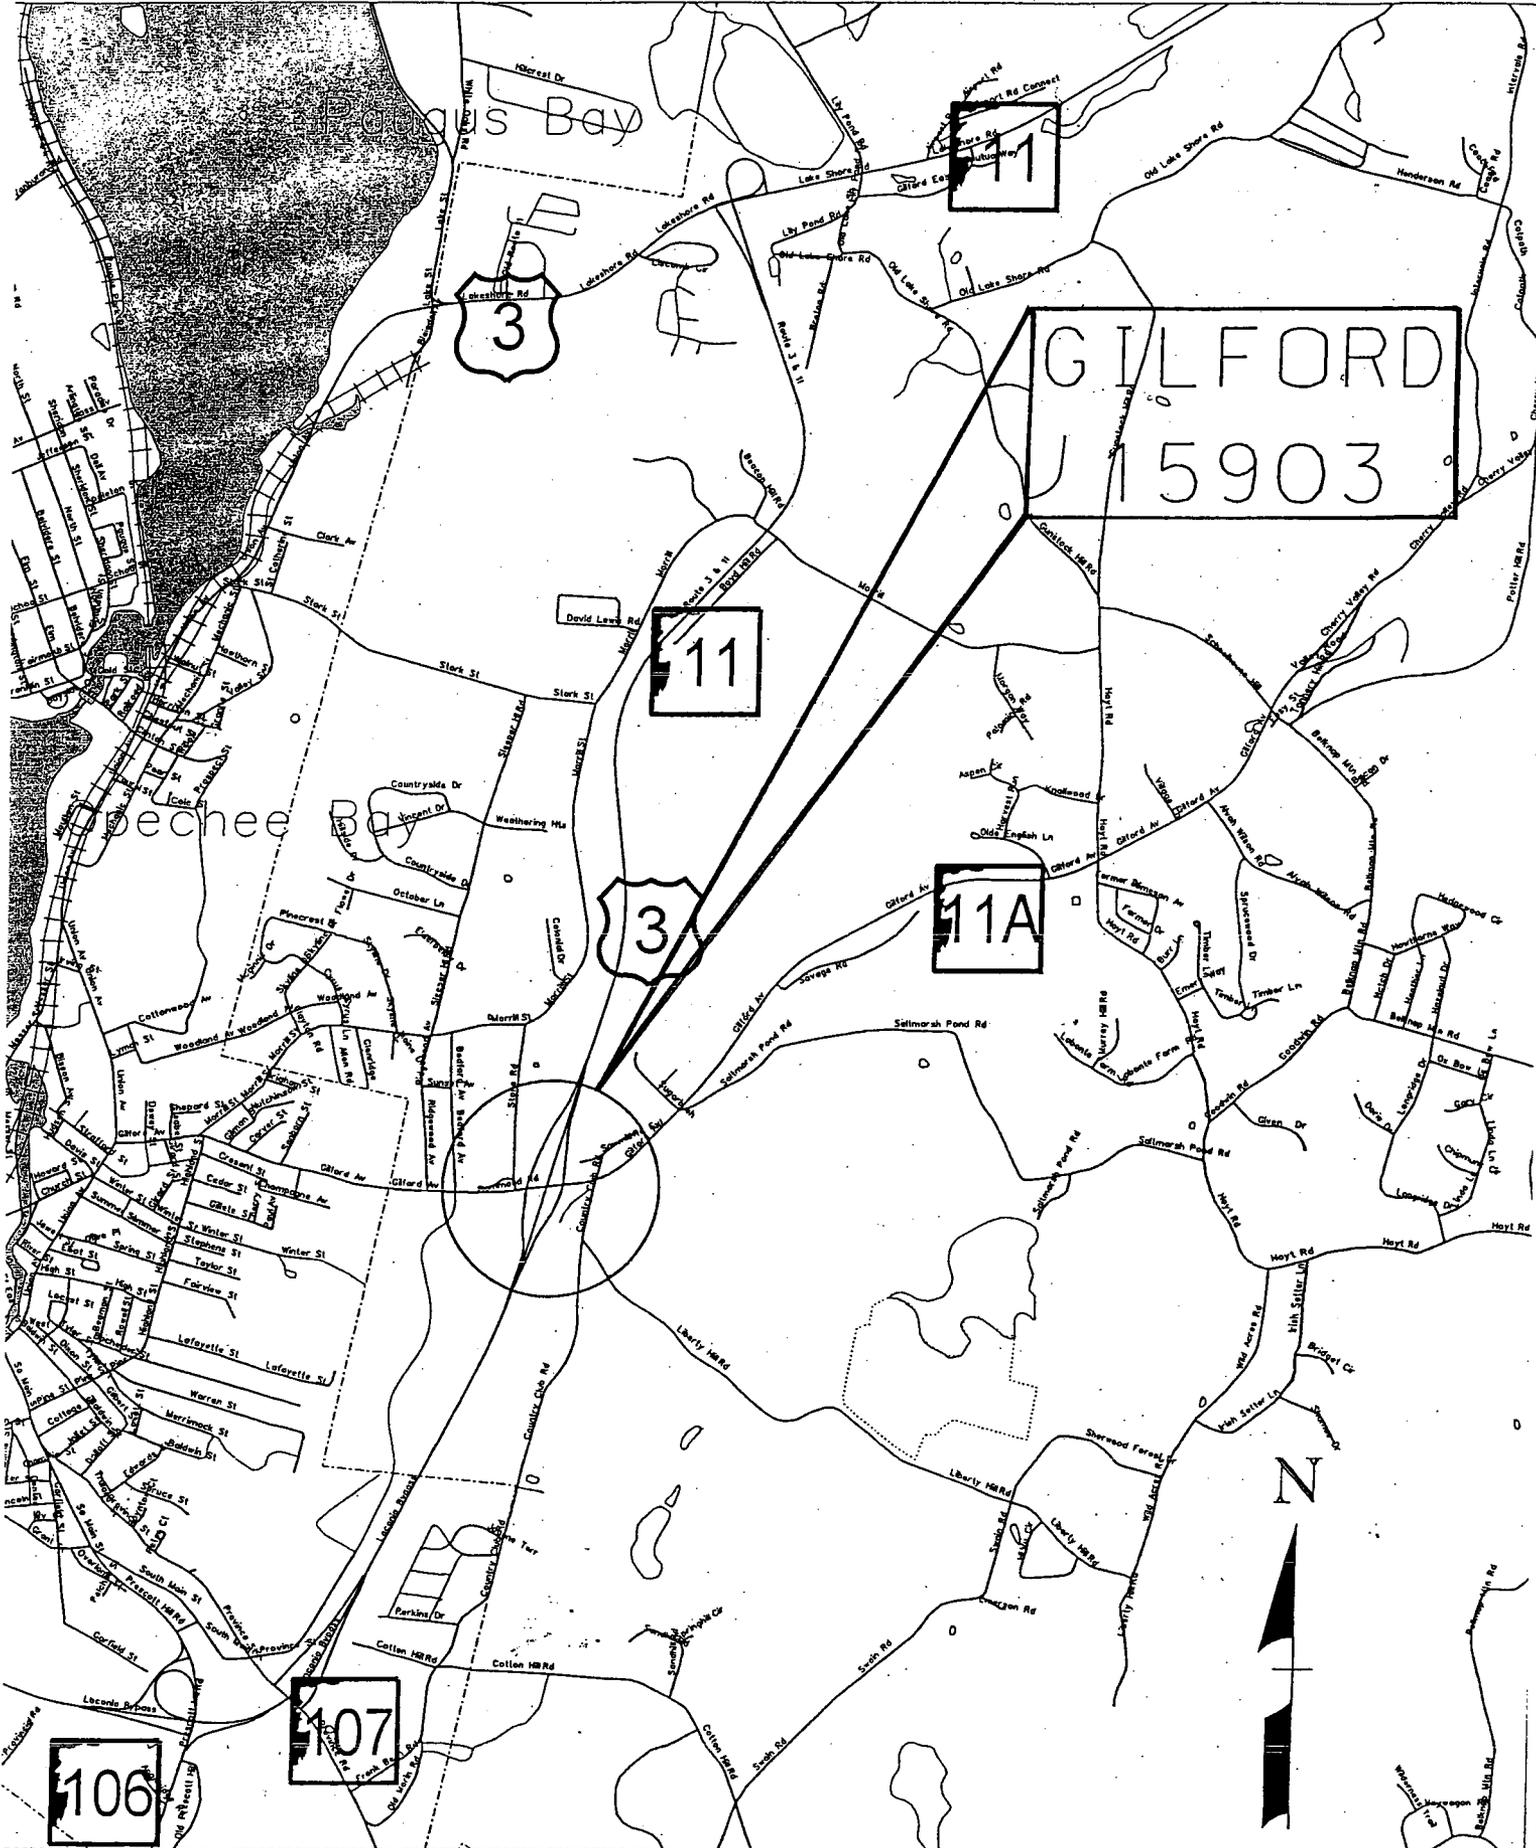

Otis Bay

Pechee Bay

GILFORD  
NH 03033

3

11

11A

107

106

N

**State of New Hampshire  
Department of Transportation**

15903.02

**Project:** GILFORD X-A001(025) 15903  
**County and Code:** BELKNAP COUNTY 001  
**Date Bids Open:** December 4, 2014  
**Scope of Work:** RAPID BRIDGE DECK REPLACEMENT  
**Location:** US ROUTE 3/NH ROUTE 11 BYPASS OVER NH ROUTE 11A  
**Completion Date:** August 5, 2016

A BECK & BELLUCCI, INC.  
PO BOX 429, 10 SALISBURY ROAD FRANKLIN, NH 03235 \$1,572,551.00

B EVROKS CORP.  
PO BOX 669 WINNISQUAM, NH 03289 \$2,225,156.65

C GEORGE R. CAIRNS AND SONS, INC.  
8 LEDGE RD., WINDHAM, NH 03087 \$2,548,807.55

D E. D. SWETT, INC.  
8 INDUSTRIAL PARK DR. CONCORD, NH 03301 \$2,554,978.50

E NEW ENGLAND INFRASTRUCTURE, INC.  
13 BRENT DRIVE HUDSON MA 01749 \$2,698,643.45

Item No:	Description	Unit	Quantity	A		B		C	
				Unit Price	Total	Unit Price	Total	Unit Price	Total
202.341	REMOVAL AND HANDLING/ SEGREGATING SOLID WASTE (<1% ASBESTOS)	CY	25.00	\$288.00	\$7,200.00	\$300.00	\$7,500.00	\$355.00	\$8,875.00
202.6	CURB REMOVAL FOR STORAGE	LF	116.00	\$10.00	\$1,160.00	\$5.00	\$580.00	\$14.00	\$1,624.00
203.5525	PORTABLE CHANGEABLE MESSAGE SIGN PLATFORM	U	4.00	\$1,000.00	\$4,000.00	\$800.00	\$3,200.00	\$1,500.00	\$6,000.00
304.3	CRUSHED GRAVEL (F)	CY	8.00	\$100.00	\$800.00	\$100.00	\$800.00	\$100.00	\$800.00
403.11	HOT BITUMINOUS PAVEMENT, MACHINE METHOD	TON	254.00	\$195.00	\$49,530.00	\$225.00	\$57,150.00	\$200.00	\$50,800.00
403.12	HOT BITUMINOUS PAVEMENT, HAND METHOD	TON	12.00	\$155.00	\$1,860.00	\$450.00	\$5,400.00	\$160.00	\$1,920.00
403.6	PAVEMENT JOINT ADHESIVE	LF	1,367.00	\$1.50	\$2,050.50	\$1.00	\$1,367.00	\$1.15	\$1,572.05
403.911	HOT BITUMINOUS BRIDGE PAVEMENT, 1" BASE COURSE	TON	24.00	\$255.00	\$6,120.00	\$350.00	\$8,400.00	\$264.00	\$6,336.00
403.99	TEMPORARY BITUMINOUS PAVEMENT	TON	68.00	\$195.00	\$13,260.00	\$250.00	\$17,000.00	\$200.00	\$13,600.00
417	COLD PLANING BITUMINOUS SURFACES	SY	200.00	\$7.75	\$1,550.00	\$25.00	\$5,000.00	\$8.00	\$1,600.00
502	REMOVAL OF EXISTING BRIDGE STRUCTURE	U	1.00	\$225,000.00	\$225,000.00	\$122,000.00	\$122,000.00	\$200,000.00	\$200,000.00
504.1	COMMON BRIDGE EXCAVATION (F)	CY	11.00	\$50.00	\$550.00	\$100.00	\$1,100.00	\$73.00	\$803.00
520.7002	CONCRETE BRIDGE DECK (QC/QA) (F)	CY	28.00	\$1,200.00	\$33,600.00	\$2,000.00	\$56,000.00	\$1,165.00	\$32,620.00
520.70061	CONCRETE BRIDGE DECK (HIGH EARLY STRENGTH) (ACC. BRIDGE CONST.) (F)	CY	7.00	\$5,000.00	\$35,000.00	\$10,000.00	\$70,000.00	\$1,465.00	\$10,255.00
528.61	PRESTRESSED CONCRETE DECK PANELS, PRE-TENSIONED AND POST-TENSIONED (F)	SF	3,966.00	\$104.00	\$412,464.00	\$263.50	\$1,045,041.00	\$310.00	\$1,229,460.00
534.3	WATER REPELLENT (SILANE/SILOXANE)	GAL	8.00	\$100.00	\$800.00	\$100.00	\$800.00	\$59.00	\$472.00

Item No:	Description	Unit	Quantity	A		B		C	
				Unit Price	Total	Unit Price	Total	Unit Price	Total
538.5	BARRIER MEMBRANE, HEAT WELDED (F)	SY	410.00	\$21.00	\$8,610.00	\$20.00	\$8,200.00	\$22.00	\$9,020.00
541.5	PVC WATERSTOPS, NH TYPE 5 (F)	LF	55.00	\$10.00	\$550.00	\$10.00	\$550.00	\$15.00	\$825.00
544	REINFORCING STEEL (F)	LB	2,181.00	\$4.00	\$8,724.00	\$5.25	\$11,450.25	\$3.00	\$6,543.00
544.11	REINFORCING STEEL-MECHANICAL CONNECTORS (F)	LB	79.00	\$10.00	\$790.00	\$10.00	\$790.00	\$15.00	\$1,185.00
544.2	REINFORCING STEEL, EPOXY COATED (F)	LB	1,637.00	\$4.00	\$6,548.00	\$2.00	\$3,274.00	\$3.10	\$5,074.70
547	SHEAR CONNECTORS (F)	EA	1,428.00	\$9.00	\$12,852.00	\$8.00	\$11,424.00	\$8.35	\$11,923.80
559.4001	ASPHALTIC PLUG EXPANSION JOINT (F)	LF	49.00	\$140.00	\$6,860.00	\$128.00	\$6,272.00	\$147.00	\$7,203.00
559.4101	ASPHALTIC PLUG FOR CRACK CONTROL (F)	LF	49.00	\$123.00	\$6,027.00	\$112.00	\$5,488.00	\$128.00	\$6,272.00
563.22	BRIDGE RAIL T2	LF	163.00	\$108.00	\$17,604.00	\$99.00	\$16,137.00	\$100.00	\$16,300.00
563.223	BRIDGE RAIL T2 WITH SNOW SCREENING	LF	157.00	\$154.00	\$24,178.00	\$141.00	\$22,137.00	\$156.00	\$24,492.00
565.222	BRIDGE APPROACH RAIL T2 (STEEL POSTS)	U	4.00	\$4,700.00	\$18,800.00	\$4,260.00	\$17,040.00	\$4,900.00	\$19,600.00
603.11006	6" CORR. STEEL PIPE, .064"	LF	80.00	\$30.00	\$2,400.00	\$35.00	\$2,800.00	\$19.00	\$1,520.00
603.11012	12" CORR. STEEL PIPE, .064"	LF	130.00	\$40.00	\$5,200.00	\$40.00	\$5,200.00	\$33.00	\$4,290.00
604.4	RECONSTRUCTING/ADJUSTING CATCH BASIN & DROP INLET	LF	4.00	\$750.00	\$3,000.00	\$500.00	\$2,000.00	\$510.00	\$2,040.00
606.417	PORTABLE CONCRETE BARRIER FOR TRAFFIC CONTROL	LF	1,000.00	\$34.00	\$34,000.00	\$20.00	\$20,000.00	\$23.00	\$23,000.00
606.91	RESETTING OR SETTING GUARDRAIL	LF	88.00	\$16.50	\$1,452.00	\$15.00	\$1,320.00	\$17.25	\$1,518.00
606.9523	TEMP. IMPACT ATTENUATION DEVICE (NON-REDIRECT.), TEST LEVEL 3	U	4.00	\$4,000.00	\$16,000.00	\$3,850.00	\$15,400.00	\$1,800.00	\$7,200.00
609.01	STRAIGHT GRANITE CURB	LF	209.00	\$20.35	\$4,253.15	\$30.00	\$6,270.00	\$28.75	\$6,008.75

Item No:	Description	Unit	Quantity	A		B		C	
				Unit Price	Total	Unit Price	Total	Unit Price	Total
609.5	RESET GRANITE CURB	LF	265.00	\$7.70	\$2,040.50	\$14.00	\$3,710.00	\$17.25	\$4,571.25
614.72118	2" PVC CONDUIT, SCHEDULE 80	LF	60.00	\$22.00	\$1,320.00	\$20.00	\$1,200.00	\$40.25	\$2,415.00
618.61	UNIFORMED OFFICERS WITH VEHICLE	\$	130,000.00	\$1.00	\$130,000.00	\$1.00	\$130,000.00	\$1.00	\$130,000.00
618.7	FLAGGERS	HR	500.00	\$23.00	\$11,500.00	\$24.00	\$12,000.00	\$24.00	\$12,000.00
619.1	MAINTENANCE OF TRAFFIC	U	1.00	\$65,000.00	\$65,000.00	\$25,000.00	\$25,000.00	\$30,000.00	\$30,000.00
619.25	PORTABLE CHANGEABLE MESSAGE SIGN	U	4.00	\$1,500.00	\$6,000.00	\$3,000.00	\$12,000.00	\$4,000.00	\$16,000.00
619.27	TRAILER-MOUNTED SPEED LIMIT SIGN	U	2.00	\$1,900.00	\$3,800.00	\$1,000.00	\$2,000.00	\$2,050.00	\$4,100.00
619.81	RAISED RUMBLE STRIPS (TRANSVERSE)	LF	720.00	\$12.50	\$9,000.00	\$12.00	\$8,640.00	\$5.75	\$4,140.00
628.2	SAVED BITUMINOUS PAVEMENT	LF	350.00	\$3.00	\$1,050.00	\$2.00	\$700.00	\$5.75	\$2,012.50
632.0104	RETROREFLECTIVE PAINT PAVE. MARKING, 4" LINE	LF	1,800.00	\$0.66	\$1,188.00	\$0.60	\$1,080.00	\$0.65	\$1,170.00
632.1104	PREFORMED RETROREFLECTIVE TAPE, TYPE I (REMOVABLE) 4" LINE	LF	1,309.00	\$1.75	\$2,290.75	\$1.60	\$2,094.40	\$1.80	\$2,356.20
632.1118	PREFORMED RETROREFLECTIVE TAPE, TYPE I (REMOVABLE) 18" LINE	LF	24.00	\$5.50	\$132.00	\$5.00	\$120.00	\$5.75	\$138.00
632.911	OBLITERATE PAVE. MARKING LINE, 12" WIDE & UNDER	LF	702.00	\$1.05	\$737.10	\$1.00	\$702.00	\$1.15	\$807.30
645.3	EROSION STONE	TON	100.00	\$30.00	\$3,000.00	\$45.00	\$4,500.00	\$31.00	\$3,100.00
645.531	SILT FENCE	LF	500.00	\$5.00	\$2,500.00	\$3.00	\$1,500.00	\$4.50	\$2,250.00
670.045	CONSTRUCT AND REMOVE DIVERSION	U	1.00	\$50,000.00	\$50,000.00	\$75,000.00	\$75,000.00	\$54,000.00	\$54,000.00
670.104	TEMPORARY PORTABLE LIGHTING	U	4.00	\$5,000.00	\$20,000.00	\$1,000.00	\$4,000.00	\$1,725.00	\$6,900.00
670.202	UTILITY CABINET	U	2.00	\$4,600.00	\$9,200.00	\$4,200.00	\$8,400.00	\$7,475.00	\$14,950.00

Item No:	Description	Unit	Quantity	A		B		C	
				Unit Price	Total	Unit Price	Total	Unit Price	Total
670.5	TEMPORARY SHUTTLE SERVICE	HR	60.00	\$75.00	\$4,500.00	\$75.00	\$4,500.00	\$82.00	\$4,920.00
692	MOBILIZATION	U	1.00	\$100,000.00	\$100,000.00	\$200,000.00	\$200,000.00	\$364,350.00	\$364,350.00
697.41	CRITICAL PATH METHOD (CPM) ELECTRONIC SCHEDULE	U	1.00	\$2,500.00	\$2,500.00	\$1,000.00	\$1,000.00	\$2,875.00	\$2,875.00
698.12	FIELD OFFICE TYPE B	MON	12.00	\$2,000.00	\$24,000.00	\$1,660.00	\$19,920.00	\$1,250.00	\$15,000.00
699	MISCELLANEOUS TEMPORARY EROSION AND SEDIMENT CONTROL	\$	5,000.00	\$1.00	\$5,000.00	\$1.00	\$5,000.00	\$1.00	\$5,000.00
1002.1	REPAIRS OR REPLACEMENTS AS NEEDED - BRIDGE STRUCTURES	\$	25,000.00	\$1.00	\$25,000.00	\$1.00	\$25,000.00	\$1.00	\$25,000.00
1008.53	ALTERATIONS AND ADDITIONS AS NEEDED - SOLID WASTE DISPOSAL	\$	25,000.00	\$1.00	\$25,000.00	\$1.00	\$25,000.00	\$1.00	\$25,000.00
1010.15	FUEL ADJUSTMENT	\$	20,000.00	\$1.00	\$20,000.00	\$1.00	\$20,000.00	\$1.00	\$20,000.00
1010.5	COMPLETION INCENTIVE/ DISINCENTIVE	\$	75,000.00	\$1.00	\$75,000.00	\$1.00	\$75,000.00	\$1.00	\$75,000.00
					\$1,572,551.00		\$2,225,156.65		\$2,548,807.55

Item No:	Description	Unit	Quantity	D		E		Unit Price	Total
				Unit Price	Total	Unit Price	Total		
202.341	REMOVAL AND HANDLING/ SEGREGATING SOLID WASTE (<1% ASBESTOS)	CY	25.00	\$600.00	\$15,000.00	\$150.00	\$3,750.00		
202.6	CURB REMOVAL FOR STORAGE	LF	116.00	\$10.00	\$1,160.00	\$25.00	\$2,900.00		
203.5525	PORTABLE CHANGEABLE MESSAGE SIGN PLATFORM	U	4.00	\$1,000.00	\$4,000.00	\$850.00	\$3,400.00		
304.3	CRUSHED GRAVEL (F)	CY	8.00	\$125.00	\$1,000.00	\$85.00	\$680.00		
403.11	HOT BITUMINOUS PAVEMENT, MACHINE METHOD	TON	254.00	\$150.00	\$38,100.00	\$180.00	\$45,720.00		
403.12	HOT BITUMINOUS PAVEMENT, HAND METHOD	TON	12.00	\$250.00	\$3,000.00	\$300.00	\$3,600.00		
403.6	PAVEMENT JOINT ADHESIVE	LF	1,367.00	\$1.00	\$1,367.00	\$1.20	\$1,640.40		
403.911	HOT BITUMINOUS BRIDGE PAVEMENT, 1" BASE COURSE	TON	24.00	\$250.00	\$6,000.00	\$400.00	\$9,600.00		
403.99	TEMPORARY BITUMINOUS PAVEMENT	TON	68.00	\$200.00	\$13,600.00	\$265.00	\$18,020.00		
417	COLD PLANING BITUMINOUS SURFACES	SY	200.00	\$25.00	\$5,000.00	\$40.00	\$8,000.00		
502	REMOVAL OF EXISTING BRIDGE STRUCTURE	U	1.00	\$250,000.00	\$250,000.00	\$344,000.00	\$344,000.00		
504.1	COMMON BRIDGE EXCAVATION (F)	CY	11.00	\$91.00	\$1,001.00	\$70.00	\$770.00		
520.7002	CONCRETE BRIDGE DECK (QC/QA) (F)	CY	28.00	\$1,500.00	\$42,000.00	\$1,600.00	\$44,800.00		
520.70061	CONCRETE BRIDGE DECK (HIGH EARLY STRENGTH) (ACC. BRIDGE CONST.) (F)	CY	7.00	\$6,000.00	\$42,000.00	\$2,900.00	\$20,300.00		
528.61	PRESTRESSED CONCRETE DECK PANELS, PRE-TENSIONED AND POST-TENSIONED (F)	SF	3,966.00	\$325.00	\$1,288,950.00	\$275.00	\$1,090,650.00		
534.3	WATER REPELLENT (SILANE/SILOXANE)	GAL	8.00	\$100.00	\$800.00	\$90.00	\$720.00		

D E

Item No:	Description	Unit	Quantity	Unit Price	Total	Unit Price	Total
538.5	BARRIER MEMBRANE, HEAT WELDED (F)	SY	410.00	\$20.00	\$8,200.00	\$35.00	\$14,350.00
541.5	PVC WATERSTOPS, NH TYPE 5 (F)	LF	55.00	\$20.00	\$1,100.00	\$16.00	\$880.00
544	REINFORCING STEEL (F)	LB	2,181.00	\$5.00	\$10,905.00	\$1.25	\$2,726.25
544.11	REINFORCING STEEL-MECHANICAL CONNECTORS (F)	LB	79.00	\$15.00	\$1,185.00	\$20.00	\$1,580.00
544.2	REINFORCING STEEL, EPOXY COATED (F)	LB	1,637.00	\$5.00	\$8,185.00	\$1.40	\$2,291.80
547	SHEAR CONNECTORS (F)	EA	1,428.00	\$7.00	\$9,996.00	\$10.00	\$14,280.00
559.4001	ASPHALTIC PLUG EXPANSION JOINT (F)	LF	49.00	\$150.00	\$7,350.00	\$200.00	\$9,800.00
559.4101	ASPHALTIC PLUG FOR CRACK CONTROL (F)	LF	49.00	\$100.00	\$4,900.00	\$120.00	\$5,880.00
563.22	BRIDGE RAIL T2	LF	163.00	\$125.00	\$20,375.00	\$100.00	\$16,300.00
563.223	BRIDGE RAIL T2 WITH SNOW SCREENING	LF	157.00	\$150.00	\$23,550.00	\$150.00	\$23,550.00
565.222	BRIDGE APPROACH RAIL T2 (STEEL POSTS)	U	4.00	\$5,000.00	\$20,000.00	\$5,000.00	\$20,000.00
603.11006	6" CORR. STEEL PIPE, .064"	LF	80.00	\$25.00	\$2,000.00	\$60.00	\$4,800.00
603.11012	12" CORR. STEEL PIPE, .064"	LF	130.00	\$40.00	\$5,200.00	\$70.00	\$9,100.00
604.4	RECONSTRUCTING/ADJUSTING CATCH BASIN & DROP INLET	LF	4.00	\$500.00	\$2,000.00	\$500.00	\$2,000.00
606.417	PORTABLE CONCRETE BARRIER FOR TRAFFIC CONTROL	LF	1,000.00	\$30.00	\$30,000.00	\$48.00	\$48,000.00
606.91	RESETTING OR SETTING GUARDRAIL	LF	88.00	\$10.00	\$880.00	\$18.00	\$1,584.00
606.9523	TEMP. IMPACT ATTENUATION DEVICE (NON-REDIRECT.), TEST LEVEL 3	U	4.00	\$3,500.00	\$14,000.00	\$4,000.00	\$16,000.00
609.01	STRAIGHT GRANITE CURB	LF	209.00	\$25.00	\$5,225.00	\$50.00	\$10,450.00

Item No:	Description	Unit	Quantity	Unit Price	D Total	E Total	Unit Price	Total
609.5	RESET GRANITE CURB	LF	265.00	\$15.00	\$3,975.00	\$30.00	\$7,950.00	
614.72118	2" PVC CONDUIT, SCHEDULE 80	LF	60.00	\$25.00	\$1,500.00	\$20.00	\$1,200.00	
618.61	UNIFORMED OFFICERS WITH VEHICLE	\$	130,000.00	\$1.00	\$130,000.00	\$1.00	\$130,000.00	
618.7	FLAGGERS	HR	500.00	\$30.00	\$15,000.00	\$25.00	\$12,500.00	
619.1	MAINTENANCE OF TRAFFIC	U	1.00	\$50,000.00	\$50,000.00	\$50,000.00	\$50,000.00	
619.25	PORTABLE CHANGEABLE MESSAGE SIGN	U	4.00	\$5,000.00	\$20,000.00	\$6,000.00	\$24,000.00	
619.27	TRAILER-MOUNTED SPEED LIMIT SIGN	U	2.00	\$2,500.00	\$5,000.00	\$6,000.00	\$12,000.00	
619.81	RAISED RUMBLE STRIPS (TRANSVERSE)	LF	720.00	\$8.00	\$5,760.00	\$5.00	\$3,600.00	
628.2	SAWED BITUMINOUS PAVEMENT	LF	350.00	\$3.00	\$1,050.00	\$5.00	\$1,750.00	
632.0104	RETROREFLECTIVE PAINT PAVE. MARKING, 4" LINE	LF	1,800.00	\$0.25	\$450.00	\$1.00	\$1,800.00	
632.1104	PREFORMED RETROREFLECTIVE TAPE, TYPE I (REMOVABLE) 4" LINE	LF	1,309.00	\$2.50	\$3,272.50	\$3.00	\$3,927.00	
632.1118	PREFORMED RETROREFLECTIVE TAPE, TYPE I (REMOVABLE) 18" LINE	LF	24.00	\$10.00	\$240.00	\$8.00	\$192.00	
632.911	OBLITERATE PAVE. MARKING LINE, 12" WIDE & UNDER	LF	702.00	\$1.00	\$702.00	\$1.00	\$702.00	
645.3	EROSION STONE	TON	100.00	\$25.00	\$2,500.00	\$40.00	\$4,000.00	
645.531	SILT FENCE	LF	500.00	\$4.00	\$2,000.00	\$8.00	\$4,000.00	
670.045	CONSTRUCT AND REMOVE DIVERSION	U	1.00	\$50,000.00	\$50,000.00	\$150,000.00	\$150,000.00	
670.104	TEMPORARY PORTABLE LIGHTING	U	4.00	\$2,500.00	\$10,000.00	\$6,000.00	\$24,000.00	
670.202	UTILITY CABINET	U	2.00	\$3,500.00	\$7,000.00	\$6,000.00	\$12,000.00	

Item No:	Description	Unit	Quantity	D		E	
				Unit Price	Total	Unit Price	Total
670.5	TEMPORARY SHUTTLE SERVICE	HR	60.00	\$75.00	\$4,500.00	\$65.00	\$3,900.00
692	MOBILIZATION	U	1.00	\$175,000.00	\$175,000.00	\$250,000.00	\$250,000.00
697.41	CRITICAL PATH METHOD (CPM) ELECTRONIC SCHEDULE	U	1.00	\$5,000.00	\$5,000.00	\$25,000.00	\$25,000.00
698.12	FIELD OFFICE TYPE B	MON	12.00	\$2,000.00	\$24,000.00	\$2,000.00	\$24,000.00
699	MISCELLANEOUS TEMPORARY EROSION AND SEDIMENT CONTROL	\$	5,000.00	\$1.00	\$5,000.00	\$1.00	\$5,000.00
1002.1	REPAIRS OR REPLACEMENTS AS NEEDED - BRIDGE STRUCTURES	\$	25,000.00	\$1.00	\$25,000.00	\$1.00	\$25,000.00
1008.53	ALTERATIONS AND ADDITIONS AS NEEDED - SOLID WASTE DISPOSAL	\$	25,000.00	\$1.00	\$25,000.00	\$1.00	\$25,000.00
1010.15	FUEL ADJUSTMENT	\$	20,000.00	\$1.00	\$20,000.00	\$1.00	\$20,000.00
1010.5	COMPLETION INCENTIVE/ DISINCENTIVE	\$	75,000.00	\$1.00	\$75,000.00	\$1.00	\$75,000.00
					\$2,554,978.50		\$2,698,643.45

# A - PS&E Comparison

PS&E = NHDOT Cost Estimate

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		Difference
				Unit Price	Total	Unit Price	Total	
202.341	REMOVAL AND HANDLING/ SEGREGATING SOLID WASTE (<1% ASBESTOS)	CY	25.00	\$288.00	\$7,200.00	\$300.00	\$7,500.00	(\$300.00)
202.6	CURB REMOVAL FOR STORAGE	LF	116.00	\$10.00	\$1,160.00	\$5.00	\$580.00	\$580.00
203.5525	PORTABLE CHANGEABLE MESSAGE SIGN PLATFORM	U	4.00	\$1,000.00	\$4,000.00	\$750.00	\$3,000.00	\$1,000.00
304.3	CRUSHED GRAVEL (F)	CY	8.00	\$100.00	\$800.00	\$30.00	\$240.00	\$560.00
403.11	HOT BITUMINOUS PAVEMENT, MACHINE METHOD	TON	254.00	\$195.00	\$49,530.00	\$75.00	\$19,050.00	\$30,480.00
403.12	HOT BITUMINOUS PAVEMENT, HAND METHOD	TON	12.00	\$155.00	\$1,860.00	\$125.00	\$1,500.00	\$360.00
403.6	PAVEMENT JOINT ADHESIVE	LF	1,367.00	\$1.50	\$2,050.50	\$2.50	\$3,417.50	(\$1,367.00)
403.911	HOT BITUMINOUS BRIDGE PAVEMENT, 1" BASE COURSE	TON	24.00	\$255.00	\$6,120.00	\$160.00	\$3,840.00	\$2,280.00
403.99	TEMPORARY BITUMINOUS PAVEMENT	TON	68.00	\$195.00	\$13,260.00	\$60.00	\$4,080.00	\$9,180.00
417	COLD PLANING BITUMINOUS SURFACES	SY	200.00	\$7.75	\$1,550.00	\$15.00	\$3,000.00	(\$1,450.00)
502	REMOVAL OF EXISTING BRIDGE STRUCTURE	U	1.00	\$225,000.00	\$225,000.00	\$60,300.00	\$60,300.00	\$164,700.00
504.1	COMMON BRIDGE EXCAVATION (F)	CY	11.00	\$50.00	\$550.00	\$15.00	\$165.00	\$385.00
520.7002	CONCRETE BRIDGE DECK (QC/QA) (F)	CY	28.00	\$1,200.00	\$33,600.00	\$1,000.00	\$28,000.00	\$5,600.00
520.70061	CONCRETE BRIDGE DECK (HIGH EARLY STRENGTH) (ACC. BRIDGE CONST.) (F)	CY	7.00	\$5,000.00	\$35,000.00	\$5,000.00	\$35,000.00	\$0.00
528.61	PRESTRESSED CONCRETE DECK PANELS, PRE-TENSIONED AND POST-TENSIONED (F)	SF	3,966.00	\$104.00	\$412,464.00	\$165.00	\$654,390.00	(\$241,926.00)
534.3	WATER REPELLENT (SILANE/SILOXANE)	GAL	8.00	\$100.00	\$800.00	\$100.00	\$800.00	\$0.00

# A - PS&E Comparison

PS&E = NHDOT Cost Estimate

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		A-PS&E Difference
				Unit Price	Total	Unit Price	Total	
538.5	BARRIER MEMBRANE, HEAT WELDED (F)	SY	410.00	\$21.00	\$8,610.00	\$25.00	\$10,250.00	(\$1,640.00)
541.5	PVC WATERSTOPS, NH TYPE 5 (F)	LF	55.00	\$10.00	\$550.00	\$10.00	\$550.00	\$0.00
544	REINFORCING STEEL (F)	LB	2,181.00	\$4.00	\$8,724.00	\$2.00	\$4,362.00	\$4,362.00
544.11	REINFORCING STEEL-MECHANICAL CONNECTORS (F)	LB	79.00	\$10.00	\$790.00	\$6.00	\$474.00	\$316.00
544.2	REINFORCING STEEL, EPOXY COATED (F)	LB	1,637.00	\$4.00	\$6,548.00	\$4.00	\$6,548.00	\$0.00
547	SHEAR CONNECTORS (F)	EA	1,428.00	\$9.00	\$12,852.00	\$5.00	\$7,140.00	\$5,712.00
559.4001	ASPHALTIC PLUG EXPANSION JOINT (F)	LF	49.00	\$140.00	\$6,860.00	\$150.00	\$7,350.00	(\$490.00)
559.4101	ASPHALTIC PLUG FOR CRACK CONTROL (F)	LF	49.00	\$123.00	\$6,027.00	\$100.00	\$4,900.00	\$1,127.00
563.22	BRIDGE RAIL T2	LF	163.00	\$108.00	\$17,604.00	\$130.00	\$21,190.00	(\$3,586.00)
563.223	BRIDGE RAIL T2 WITH SNOW SCREENING	LF	157.00	\$154.00	\$24,178.00	\$150.00	\$23,550.00	\$628.00
565.222	BRIDGE APPROACH RAIL T2 (STEEL POSTS)	U	4.00	\$4,700.00	\$18,800.00	\$4,000.00	\$16,000.00	\$2,800.00
603.11006	6" CORR. STEEL PIPE, .064"	LF	80.00	\$30.00	\$2,400.00	\$50.00	\$4,000.00	(\$1,600.00)
603.11012	12" CORR. STEEL PIPE, .064"	LF	130.00	\$40.00	\$5,200.00	\$50.00	\$6,500.00	(\$1,300.00)
604.4	RECONSTRUCTING/ADJUSTING CATCH BASIN & DROP INLET	LF	4.00	\$750.00	\$3,000.00	\$400.00	\$1,600.00	\$1,400.00
606.417	PORTABLE CONCRETE BARRIER FOR TRAFFIC CONTROL	LF	1,000.00	\$34.00	\$34,000.00	\$20.00	\$20,000.00	\$14,000.00
606.91	RESETTING OR SETTING GUARDRAIL	LF	88.00	\$16.50	\$1,452.00	\$10.00	\$880.00	\$572.00
606.9523	TEMP. IMPACT ATTENUATION DEVICE (NON-REDIRECT.), TEST LEVEL 3	U	4.00	\$4,000.00	\$16,000.00	\$10,000.00	\$40,000.00	(\$24,000.00)
609.01	STRAIGHT GRANITE CURB	LF	209.00	\$20.35	\$4,253.15	\$20.00	\$4,180.00	\$73.15

# A - PS&E Comparison

PS&E = NHDOT Cost Estimate

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		A-PS&E Difference
				Unit Price	Total	Unit Price	Total	
609.5	RESET GRANITE CURB	LF	265.00	\$7.70	\$2,040.50	\$10.00	\$2,650.00	(\$609.50)
614.72118	2" PVC CONDUIT, SCHEDULE 80	LF	60.00	\$22.00	\$1,320.00	\$10.00	\$600.00	\$720.00
618.61	UNIFORMED OFFICERS WITH VEHICLE	\$	130,000.00	\$1.00	\$130,000.00	\$1.00	\$130,000.00	\$0.00
618.7	FLAGGERS	HR	500.00	\$23.00	\$11,500.00	\$22.00	\$11,000.00	\$500.00
619.1	MAINTENANCE OF TRAFFIC	U	1.00	\$65,000.00	\$65,000.00	\$20,000.00	\$20,000.00	\$45,000.00
619.25	PORTABLE CHANGEABLE MESSAGE SIGN	U	4.00	\$1,500.00	\$6,000.00	\$6,000.00	\$24,000.00	(\$18,000.00)
619.27	TRAILER-MOUNTED SPEED LIMIT SIGN	U	2.00	\$1,900.00	\$3,800.00	\$7,500.00	\$15,000.00	(\$11,200.00)
619.81	RAISED RUMBLE STRIPS (TRANSVERSE)	LF	720.00	\$12.50	\$9,000.00	\$10.00	\$7,200.00	\$1,800.00
628.2	SAWED BITUMINOUS PAVEMENT	LF	350.00	\$3.00	\$1,050.00	\$2.00	\$700.00	\$350.00
632.0104	RETROREFLECTIVE PAINT PAVE. MARKING, 4" LINE	LF	1,800.00	\$0.66	\$1,188.00	\$0.50	\$900.00	\$288.00
632.1104	PREFORMED RETROREFLECTIVE TAPE, TYPE I (REMOVABLE) 4" LINE	LF	1,309.00	\$1.75	\$2,290.75	\$2.00	\$2,618.00	(\$327.25)
632.1118	PREFORMED RETROREFLECTIVE TAPE, TYPE I (REMOVABLE) 18" LINE	LF	24.00	\$5.50	\$132.00	\$10.00	\$240.00	(\$108.00)
632.911	OBLITERATE PAVE. MARKING LINE, 12" WIDE & UNDER	LF	702.00	\$1.05	\$737.10	\$1.00	\$702.00	\$35.10
645.3	EROSION STONE	TON	100.00	\$30.00	\$3,000.00	\$25.00	\$2,500.00	\$500.00
645.531	SILT FENCE	LF	500.00	\$5.00	\$2,500.00	\$4.00	\$2,000.00	\$500.00
670.045	CONSTRUCT AND REMOVE DIVERSION	U	1.00	\$50,000.00	\$50,000.00	\$10,000.00	\$10,000.00	\$40,000.00
670.104	TEMPORARY PORTABLE LIGHTING	U	4.00	\$5,000.00	\$20,000.00	\$4,000.00	\$16,000.00	\$4,000.00
670.202	UTILITY CABINET	U	2.00	\$4,600.00	\$9,200.00	\$4,000.00	\$8,000.00	\$1,200.00

# A - PS&E Comparison

PS&E = NHDOT Cost Estimate

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		A-PS&E Difference
				Unit Price	Total	Unit Price	Total	
670.5	TEMPORARY SHUTTLE SERVICE	HR	60.00	\$75.00	\$4,500.00	\$100.00	\$6,000.00	(\$1,500.00)
692	MOBILIZATION	U	1.00	\$100,000.00	\$100,000.00	\$88,000.00	\$88,000.00	\$12,000.00
697.41	CRITICAL PATH METHOD (CPM) ELECTRONIC SCHEDULE	U	1.00	\$2,500.00	\$2,500.00	\$2,000.00	\$2,000.00	\$500.00
698.12	FIELD OFFICE TYPE B	MON	12.00	\$2,000.00	\$24,000.00	\$2,000.00	\$24,000.00	\$0.00
699	MISCELLANEOUS TEMPORARY EROSION AND SEDIMENT CONTROL	\$	5,000.00	\$1.00	\$5,000.00	\$1.00	\$5,000.00	\$0.00
1002.1	REPAIRS OR REPLACEMENTS AS NEEDED - BRIDGE STRUCTURES	\$	25,000.00	\$1.00	\$25,000.00	\$1.00	\$25,000.00	\$0.00
1008.53	ALTERATIONS AND ADDITIONS AS NEEDED - SOLID WASTE DISPOSAL	\$	25,000.00	\$1.00	\$25,000.00	\$1.00	\$25,000.00	\$0.00
1010.15	FUEL ADJUSTMENT	\$	20,000.00	\$1.00	\$20,000.00	\$1.00	\$20,000.00	\$0.00
1010.5	COMPLETION INCENTIVE/ DISINCENTIVE	\$	75,000.00	\$1.00	\$75,000.00	\$1.00	\$75,000.00	\$0.00
					\$1,572,551.00		\$1,528,446.50	\$44,104.50





# CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)  
12/12/2014

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

**IMPORTANT:** If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

<b>PRODUCER</b> THE ROWLEY AGENCY INC. 139 Loudon Road P.O. Box 511 Concord NH 03302-0511	<b>CONTACT NAME:</b> Christine Holman, CPCU, CIC <b>PHONE (A/C No. Ext):</b> (603) 224-2562 <b>FAX (A/C No.):</b> (603) 224-8012 <b>E-MAIL ADDRESS:</b> cholman@rowleyagency.com													
	<table border="1"> <tr> <th>INSURER(S) AFFORDING COVERAGE</th> <th>NAIC #</th> </tr> <tr> <td>INSURER A: Travelers</td> <td>28188</td> </tr> <tr> <td>INSURER B:</td> <td></td> </tr> <tr> <td>INSURER C:</td> <td></td> </tr> <tr> <td>INSURER D:</td> <td></td> </tr> <tr> <td>INSURER E:</td> <td></td> </tr> <tr> <td>INSURER F:</td> <td></td> </tr> </table>	INSURER(S) AFFORDING COVERAGE	NAIC #	INSURER A: Travelers	28188	INSURER B:		INSURER C:		INSURER D:		INSURER E:		INSURER F:
INSURER(S) AFFORDING COVERAGE	NAIC #													
INSURER A: Travelers	28188													
INSURER B:														
INSURER C:														
INSURER D:														
INSURER E:														
INSURER F:														
<b>INSURED</b> Beck & Bellucci Inc. Miller Construction Inc. P.O. Box 429 Franklin NH 03235-0429														

**COVERAGES**      **CERTIFICATE NUMBER: 14-15 B & B**      **REVISION NUMBER:**

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL INSR	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	GENERAL LIABILITY <input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR			DTCO2572L87A	6/30/2014	6/30/2015	EACH OCCURRENCE \$ 1,000,000 DAMAGE TO RENTED PREMISES (Ea occurrence) \$ 300,000 MED EXP (Any one person) \$ 5,000 PERSONAL & ADV INJURY \$ 1,000,000 GENERAL AGGREGATE \$ 2,000,000 PRODUCTS - COM/OP AGG \$ 2,000,000
	GEN'L AGGREGATE LIMIT APPLIES PER: <input checked="" type="checkbox"/> POLICY <input checked="" type="checkbox"/> PROJ <input type="checkbox"/> LOC						
A	AUTOMOBILE LIABILITY <input checked="" type="checkbox"/> ANY AUTO <input type="checkbox"/> ALL OWNED AUTOS <input type="checkbox"/> HIRED AUTOS <input type="checkbox"/> SCHEDULED AUTOS <input type="checkbox"/> NON-OWNED AUTOS			DT8102572L87ACOF14	6/30/2014	6/30/2015	COMBINED SINGLE LIMIT (Ea accident) \$ 1,000,000 BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$ Uninsured motorist combined \$ 1,000,000
A	UMBRELLA LIAB <input checked="" type="checkbox"/> OCCUR EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE DED <input checked="" type="checkbox"/> RETENTION \$ 0			DTSMCUP2572L87A	6/30/2014	6/30/2015	EACH OCCURRENCE \$ 10,000,000 AGGREGATE \$ 10,000,000
A	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) If yes, describe under DESCRIPTION OF OPERATIONS below		N/A	3A States: NH, VT DTEUB4436L35614	6/30/2014	6/30/2015	<input checked="" type="checkbox"/> WC STATUTORY LIMITS <input type="checkbox"/> OTHER E.L. EACH ACCIDENT \$ 500,000 E.L. DISEASE - EA EMPLOYEE \$ 500,000 E.L. DISEASE - POLICY LIMIT \$ 500,000
A	Leased/Rented Equipment Riggers Liability			QT6603083B737 QT6603083B737	6/30/2014 6/30/2014	6/30/2015 6/30/2015	Limit 500,000 Limitr 300,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (Attach ACORD 101, Additional Remarks Schedule, if more space is required)  
 re: Gilford X-A001(025), 15903 Rapid Deck replacement of the US Route 3/NH Route 11 Bypass (BR No. 160/053) over NH Routa 11A Certificate holder is included as an additional insured under general liability coverage when required by written contract

<b>CERTIFICATE HOLDER</b>  State of NH Department of Transportation PO Box 483 Concord, NH 03302-0483	<b>CANCELLATION</b>  SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.
	<b>AUTHORIZED REPRESENTATIVE</b>  C Holman, CPCU, CIC/C <i>Christie Holman</i>



# CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)  
12/12/2014

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

**IMPORTANT:** If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

<b>PRODUCER</b> THE ROWLEY AGENCY INC. 139 Loudon Road P.O. Box 511 Concord NH 03302-0511	<b>CONTACT NAME:</b> Christine Holman, CPCU, CIC	
	<b>PHONE (A/C No. Ext):</b> (603) 224-2562	<b>FAX (A/C No.):</b> (603) 224-8012
<b>E-MAIL ADDRESS:</b> cholman@rowleyagency.com		
<b>INSURER(S) AFFORDING COVERAGE</b>		<b>NAIC #</b>
<b>INSURER A:</b> Travelers		28188
<b>INSURER B:</b>		
<b>INSURER C:</b>		
<b>INSURER D:</b>		
<b>INSURER E:</b>		
<b>INSURER F:</b>		

**COVERAGES**                      **CERTIFICATE NUMBER:** OCP - Gilford                      **REVISION NUMBER:**

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL INSR	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	<b>GENERAL LIABILITY</b> <input type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input type="checkbox"/> OCCUR <input checked="" type="checkbox"/> OCP			OCP010715	01/07/2015	01/07/2016	EACH OCCURRENCE \$ 2,000,000 DAMAGE TO RENTED PREMISES (Ea occurrence) \$ MED EXP (Any one person) \$ PERSONAL & ADV INJURY \$ GENERAL AGGREGATE \$ 3,000,000 PRODUCTS - COMP/OP AGG \$ \$
	GEN'L AGGREGATE LIMIT APPLIES PER: <input checked="" type="checkbox"/> POLICY <input type="checkbox"/> PRO. JECT <input type="checkbox"/> LOC						
	<b>AUTOMOBILE LIABILITY</b> <input type="checkbox"/> ANY AUTO <input type="checkbox"/> ALL OWNED AUTOS <input type="checkbox"/> SCHEDULED AUTOS <input type="checkbox"/> HIRED AUTOS <input type="checkbox"/> NON-OWNED AUTOS						
	<b>UMBRELLA LIAB</b> <input type="checkbox"/> OCCUR <b>EXCESS LIAB</b> <input type="checkbox"/> CLAIMS-MADE <input type="checkbox"/> DED <input type="checkbox"/> RETENTION \$						
<b>WORKERS COMPENSATION AND EMPLOYERS' LIABILITY</b> ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) <input type="checkbox"/> Y <input checked="" type="checkbox"/> N If yes, describe under DESCRIPTION OF OPERATIONS below							
WC STATUTORY LIMITS    OTH-ER E.L. EACH ACCIDENT \$ E.L. DISEASE - EA EMPLOYEE \$ E.L. DISEASE - POLICY LIMIT \$							

**DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES** (Attach ACORD 101, Additional Remarks Schedule, if more space is required)  
 Gilford X-A001(025), 15903 Rapid Deck replacement of the US Route 3/NH Route 11 Bypass (BR No. 160/053) over NH Route 11A

<b>CERTIFICATE HOLDER</b>  State of NH Department of Transportation PO Box 483 Concord, NH 03302-0483	<b>CANCELLATION</b>  SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.
	<b>AUTHORIZED REPRESENTATIVE</b>  C Holman, CPCU, CIC/C <i>Christine Holman</i>
